


3/3017/94
8 (A)
set I

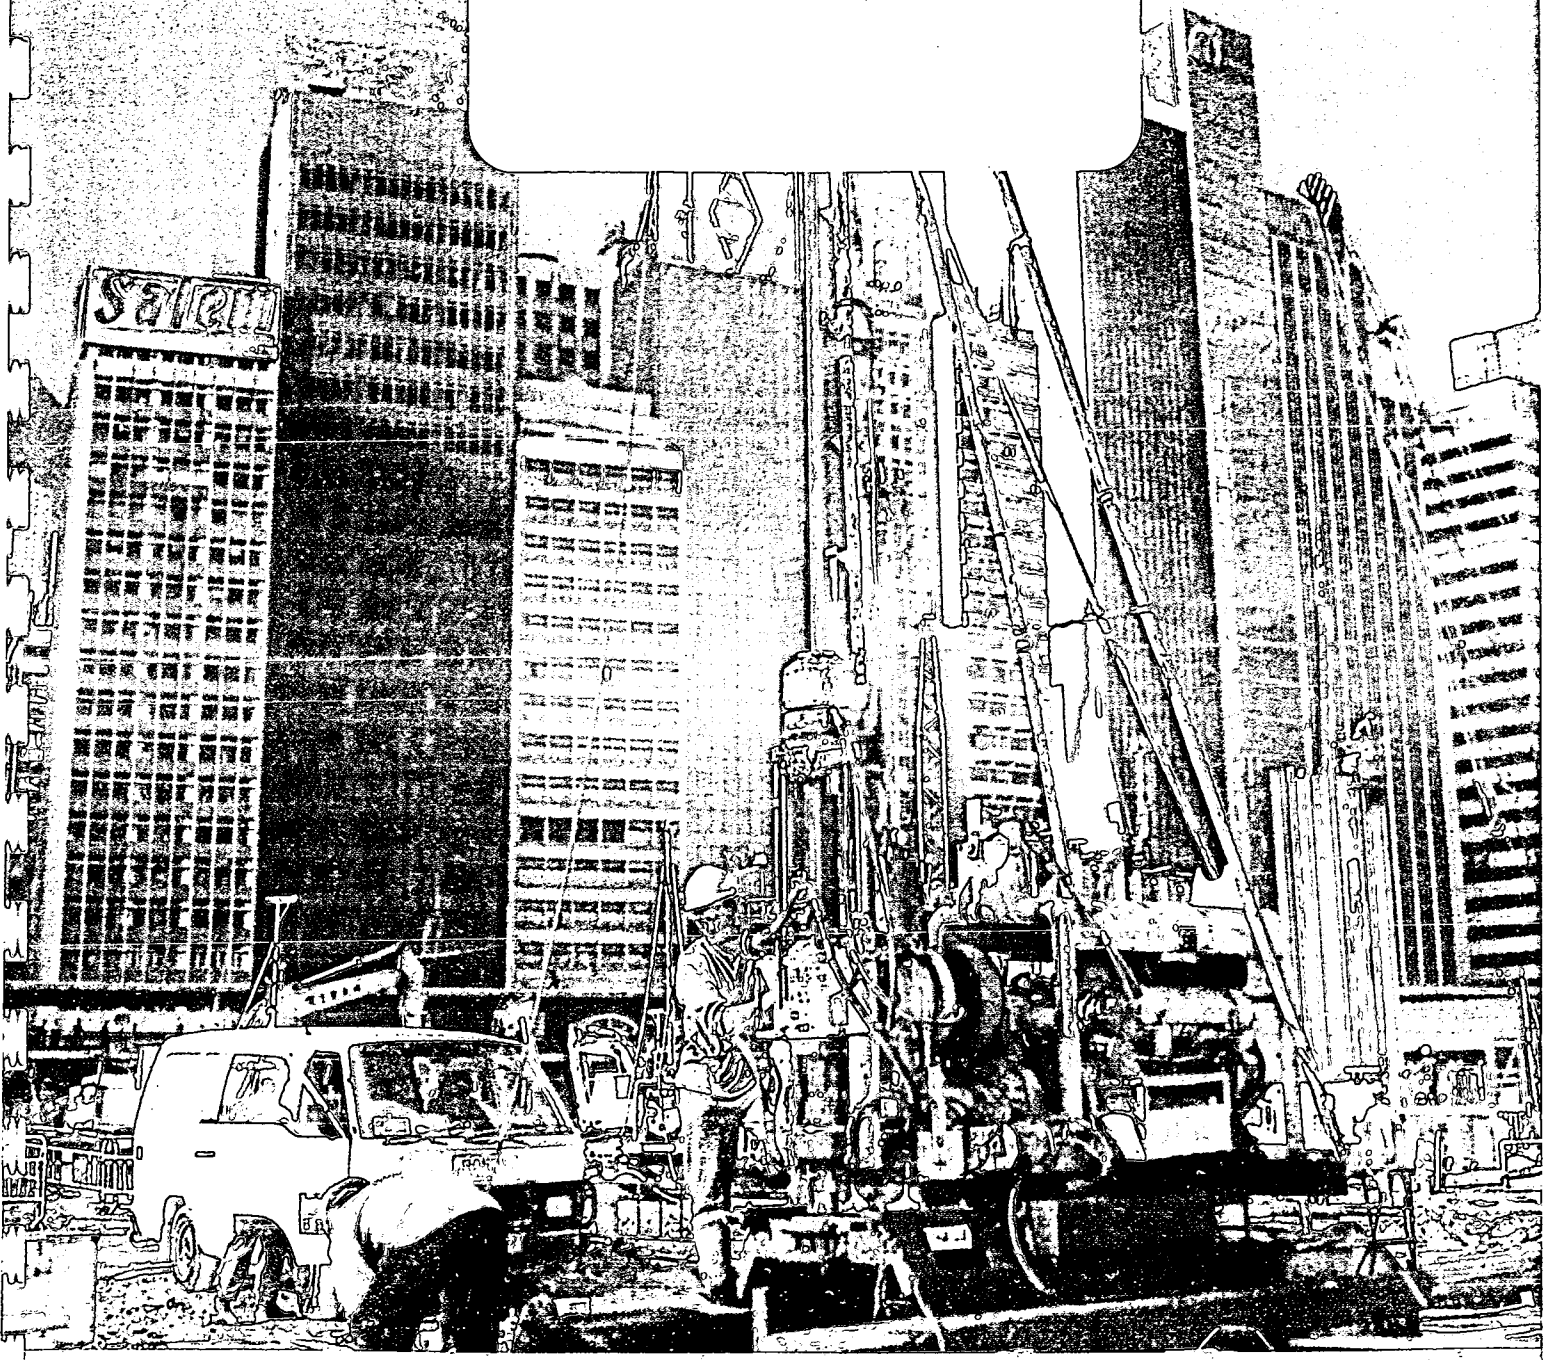

**BACHY
SOLETANCHE**

泰國地基建築公司

BACHY SOLETANCHE GROUP
SOIL & FOUNDATION SPECIALISTS



ISO 9001: 1994
Certificate No: CC295

**BACHY
SOLETANCHE**



LINCOLN HOUSE DEVELOPMENT, QUARRY BAY

SITE INVESTIGATION
FOR
DIAPHRAGM WALL AND BARRETTES

(HOLE NOS. P1, P2, P3, P4, P61,
P62, P63, P64, B6a, B6b & C6a)

Ref 3/3017/94

AUGUST, 1996

BACHY SOLETANCHE
BUILDINGS DEPARTMENT

SEP 23 3 49 PM '96

RECEIVED BY

CONTRACTOR

BACHY SOLETANCHE GROUP
15/F., CARNARVON PLAZA
20-20C CARNARVON ROAD
TSIM SHA TSUI
KOWLOON
HONG KONG

ENGINEER

MAUNSELL CONSULTANTS ASIA LTD
14/F., 1 KOWLOON PARK DRIVE
KOWLOON
HONG KONG



BACHY SOLETANCHE GROUP
SOIL & FOUNDATIONS SPECIALISTS

DRILLHOLE RECORD

HOLE NO. P1

SHEET 1 of 4

CONTRACT

PROJECT LINCOLN HOUSE DEVELOPMENT, QUARRY BAY

METHOD ROTARY

CO-ORDINATES

W.O. W-518

MACHINE & No. D-16

E 839893.54
N 816492.21

DATE from 16/7/96 to 17/7/96

FLUSHING MEDIUM WATER

ORIENTATION Vertical

GROUND-LEVEL 4.72 mPD

Drilling Progress	Casing size	Water level (m) Shift start/end	Total core Recovery %	Solid core Recovery %	R.Q.D.	Fracture Index	Tests	Samples	Reduced Level	Depth (m)	Legend	Grade	Description
1	PX												0.00-3.00m: wash boring
2													
3	PX 3.00m HX		83					PX	1.72 1.42	3.00 3.30			Rounded and subrounded COBBLES, fine to coarse GRAVEL and CONCRETE. (FILL) 3.30-17.00m: washed boring
4													
5													
6													
7													
8													
9													
10													

- SMALL DISTURBED SAMPLE
- ▮ LARGE DISTURBED SAMPLE
- ▮ SPT LIVER SAMPLE
- ▮ U76 UNDISTURBED SAMPLE
- ▮ U100 UNDISTURBED SAMPLE
- ▮ MAZIER SAMPLE (70mm)
- ▮ PISTON SAMPLE
- △ WATER SAMPLE
- ▲ PIEZOMETER TIP
- STANDPIPE
- ┃ STANDARD PENETRATION TEST
- ┃ PERMEABILITY TEST
- ∨ IN-SITU VANE SHEAR TEST

LOGGED BENNY WONG

DATE 23/7/96

APPROVED C. LUN

DATE 24/7/96

REMARKS

Hole termination depth at 30.91m.



BACHY SOLETANCHE GROUP
SOIL & FOUNDATIONS SPECIALISTS

DRILLHOLE RECORD

HOLE NO. P1

CONTRACT

SHEET 2 of 4

PROJECT LINCOLN HOUSE DEVELOPMENT, QUARRY BAY

METHOD ROTARY

CO-ORDINATES

W.O. W-518

MACHINE & No. D-16

E 839893.54
N 816492.21

DATE from 16/7/96 to 17/7/96

FLUSHING MEDIUM WATER

ORIENTATION Vertical

GROUND-LEVEL 4.72 mPD

Drilling Progress	Casing size	Water level (m) Shift start/end	Total core Recovery %	Solid core Recovery %	R.Q.D.	Fracture Index	Tests	Samples	Reduced Level	Depth (m)	Legend	Grade	Description
11													AS SHEET 1 OF 4
12													
13													
14													
15													Rounded and subrounded COBBLES and fine to coarse GRAVEL. No recovery assumed finer material washed out. 17.50-24.98m: wash boring
16													
17	HX 17.00m NX	3.50m at 19:30	50					T2-101	-12.28	17.00	0 0		
18		5.50m at 07:30							-12.78	17.50	0 0		
19													
20													

- SMALL DISTURBED SAMPLE
- LARGE DISTURBED SAMPLE
- SPT LINER SAMPLE
- U76 UNDISTURBED SAMPLE
- U100 UNDISTURBED SAMPLE
- MAZIER SAMPLE (70mm)
- PISTON SAMPLE
- WATER SAMPLE
- PIEZOMETER TIP
- STANDPIPE
- STANDARD PENETRATION TEST
- PERMEABILITY TEST
- IN-SITU VANE SHEAR TEST

LOGGED BENNY WONG
DATE 23/7/96
APPROVED C. LUN
DATE 24/7/96

REMARKS



BACHY SOLETANCHE GROUP
SOIL & FOUNDATIONS SPECIALISTS

DRILLHOLE RECORD

HOLE NO. P1

CONTRACT

SHEET 3 of 4

PROJECT LINCOLN HOUSE DEVELOPMENT, QUARRY BAY

METHOD ROTARY

CO-ORDINATES

W.O. W-518

MACHINE & No. D-16

E 839893.54
N 816492.21

DATE from 16/7/96 to 17/7/96

FLUSHING MEDIUM WATER

ORIENTATION Vertical

GROUND-LEVEL 4.72 mPD

Drilling Progress	Casing size	Water level (m) Shift start/end	Total core Recovery %	Solid core Recovery %	R.Q.D.	Fracture Index	Tests	Samples	Reduced Level	Depth (m)	Legend	Grade	Description
21													AS SHEET 2 OF 4
22													
23													
24													
25	NX	24.98m							-20.26	24.98			
25			99	99	40			TNW			+++	III/IV	Moderately strong to moderately weak, brownish grey, spotted black and yellow, moderately to highly decomposed, medium grained GRANITE with closely spaced, narrow to very narrow, limonite and manganese stained joints, dipping 15° to 35°.
26			100	100	100			TNW		25.92	+++		
27			99	99	89	10.6		TNW		26.72	+++		
28			100	100	52			TNW		27.76	+++		Strong, pinkish grey, spotted black and white, slightly decomposed medium grained GRANITE with closely to medium spaced, very narrow, rough undulating, clean joints, dipping 5° to 10°.
29			100	100	88			TNW	-23.66	28.38	+++	II	
30						4.0		TNW		29.57	+++		

- SMALL DISTURBED SAMPLE
- ▬ LARGE DISTURBED SAMPLE
- ▬ SPT LINER SAMPLE
- ▬ U76 UNDISTURBED SAMPLE
- ▬ U100 UNDISTURBED SAMPLE
- ▬ MAZIER SAMPLE (70mm)
- ▬ PISTON SAMPLE
- Δ WATER SAMPLE
- ▲ PIEZOMETER TIP
- STANDPIPE
- ↓ STANDARD PENETRATION TEST
- ⊥ PERMEABILITY TEST
- ∇ IN-SITU VANE SHEAR TEST

LOGGED BENNY WONG

DATE 23/7/96

APPROVED C. LUN

DATE 24/7/96

REMARKS



BACHY SOLETANCHE GROUP
SOIL & FOUNDATIONS SPECIALISTS

DRILLHOLE RECORD

CONTRACT

HOLE NO. P1

SHEET 4 of 4

PROJECT LINCOLN HOUSE DEVELOPMENT, QUARRY BAY

METHOD ROTARY

CO-ORDINATES

W.O. W-518

MACHINE & No. D-16

E 839893.54
N 816492.21

DATE from 16/7/96 to 17/7/96

FLUSHING MEDIUM WATER

ORIENTATION Vertical



GROUND-LEVEL 4.72 mPD

Drilling Progress	Casing size	Water level (m) Shift start/end	Total core Recovery %	Solid core Recovery %	R.Q.D.	Fracture Index	Tests	Samples	Reduced Level	Depth (m)	Legend	Grade	Description
17/7/96			100	100	96			↑ TNW ↓	-26.19	30.91	++++ ++++ ++++ ++++		AS SHEET 3 OF 4
31													End of hole at 30.91m.
32													
33													
34													
35													
36													
37													
38													
39													
40													

- SMALL DISTURBED SAMPLE
- LARGE DISTURBED SAMPLE
- SPT LINER SAMPLE
- U76 UNDISTURBED SAMPLE
- U100 UNDISTURBED SAMPLE
- MAZIER SAMPLE (70mm)
- PISTON SAMPLE
- WATER SAMPLE
- PIEZOMETER TIP
- STANDPIPE
- STANDARD PENETRATION TEST
- PERMEABILITY TEST
- IN-SITU VANE SHEAR TEST

LOGGED BENNY WONG
DATE 23/7/96
APPROVED C. LUN
DATE 24/7/96

REMARKS

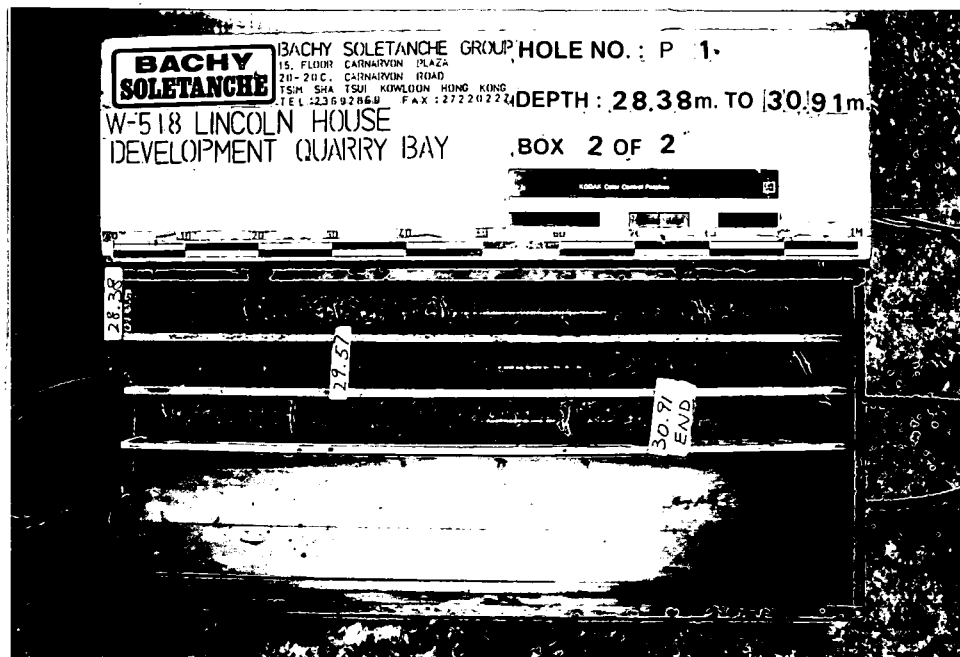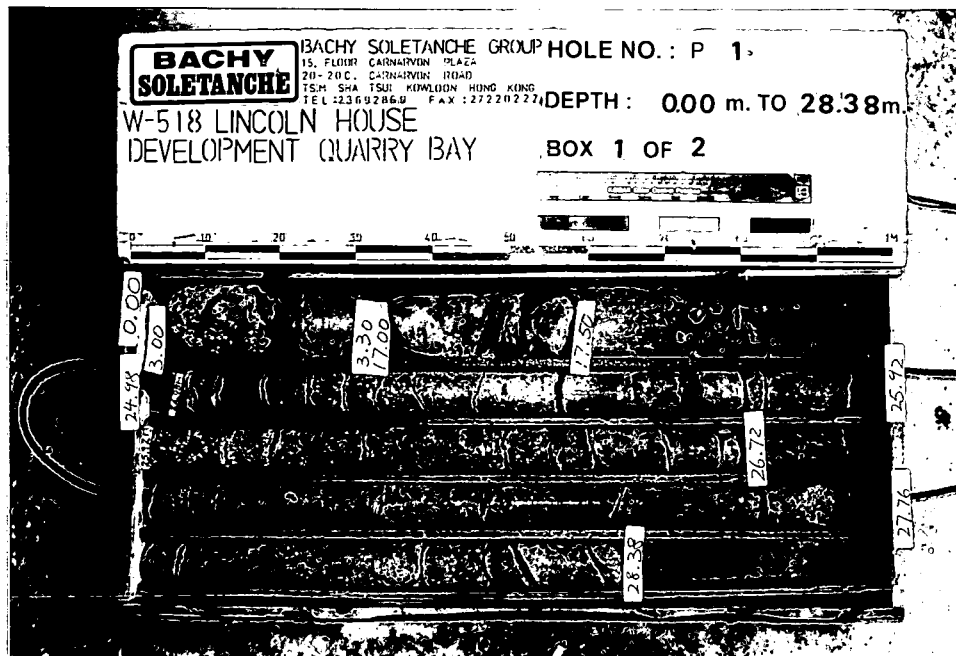



BACHY SOLETANCHE GROUP
SOIL & FOUNDATIONS SPECIALISTS

DRILLHOLE RECORD

HOLE NO. P2

SHEET 1 of 4

CONTRACT

PROJECT LINCOLN HOUSE DEVELOPMENT, QUARRY BAY

METHOD ROTARY

CO-ORDINATES

W.O. W-518

MACHINE & No. D18

E 839893.70

DATE from 16/7/96 to 19/7/96

N 816495.10

FLUSHING MEDIUM WATER

ORIENTATION Vertical

GUIDE WALL LEVEL 4.72 mPD

Drilling Progress	Casing size	Water level (m) Shift start/end	Total core Recovery %	Solid core Recovery %	R.Q.D.	Fracture Index	Tests	Samples	Reduced Level	Depth (m)	Legend	Grade	Description
1	PX							INSPECTION PIT		0.00			Wash boring.
2										2.00			
3	PX 3.30m HX								1.42	3.30			
4			89					HX		4.40			Rounded and sub-rounded COBBLES, fine to coarse GRAVEL and CONCRETE. No recovery, assumed finer material washed out. (FILL)
5			82					HX		5.75			
6			66					HX	-1.38	6.10			Wash boring.
7													
8													
9													
10													

- SMALL DISTURBED SAMPLE
- LARGE DISTURBED SAMPLE
- SPT LINER SAMPLE
- U76 UNDISTURBED SAMPLE
- U100 UNDISTURBED SAMPLE
- MAZIER SAMPLE (70mm)
- PISTON SAMPLE
- WATER SAMPLE
- PIEZOMETER TIP
- STANDPIPE
- STANDARD PENETRATION TEST
- PERMEABILITY TEST
- IN-SITU VANE SHEAR TEST

LOGGED BENNY WONG

DATE 20/07/96

APPROVED C.LUN

DATE 22/07/96

REMARKS
Hole termination depth at 30.79m.
Inspection pit from 0.00m to 2.00m.



BACHY SOLETANCHE GROUP
SOIL & FOUNDATIONS SPECIALISTS

DRILLHOLE RECORD

HOLE NO. P2

CONTRACT

SHEET 2 of 4

PROJECT LINCOLN HOUSE DEVELOPMENT, QUARRY BAY

METHOD ROTARY

CO-ORDINATES

W.O. W-518

MACHINE & No. D18

E 839893.70
N 816495.10

DATE from 16/7/96 to 19/7/96

FLUSHING MEDIUM WATER

ORIENTATION Vertical

GUIDE WALL LEVEL 4.72 mPD

Drilling Progress	Casing size	Water level (m) Shift start/end	Total core Recovery %	Solid core Recovery %	R.Q.D.	Fracture Index	Tests	Samples	Reduced Level	Depth (m)	Legend	Grade	Description
11													AS SHEET 1 OF 4.
12													
13													
14 17/07/96													
15													Rounded and sub-rounded COBBLES and fine to coarse GRAVEL. No recovery, assumed finer material washed out. (FILL) Wash boring.
16													
17													
18	HX 18.00m NX		60						-13.28 -13.78	18.00 18.50			
19 18/07/96													
20													

- SMALL DISTURBED SAMPLE
- ▬ LARGE DISTURBED SAMPLE
- ▨ SPT LINER SAMPLE
- ▩ U76 UNDISTURBED SAMPLE
- ▩ U100 UNDISTURBED SAMPLE
- ▩ MAZIER SAMPLE (70mm)
- ▩ PISTON SAMPLE
- Δ WATER SAMPLE
- ▲ PIEZOMETER TIP
- STANDPIPE
- ↓ STANDARD PENETRATION TEST
- ⊥ PERMEABILITY TEST
- ∇ IN-SITU VANE SHEAR TEST

LOGGED BENNY WONG

DATE 20/07/96

APPROVED C.LUN

DATE 22/07/96

REMARKS



BACHY SOLETANCHE GROUP
SOIL & FOUNDATIONS SPECIALISTS

DRILLHOLE RECORD

HOLE NO. P2

SHEET 3 of 4

CONTRACT

PROJECT LINCOLN HOUSE DEVELOPMENT, QUARRY BAY

METHOD ROTARY

CO-ORDINATES

W.O. W-518

MACHINE & No. D18

E 839893.70

DATE from 16/7/96 to 19/7/96

N 816495.10

FLUSHING MEDIUM WATER

ORIENTATION Vertical

GUIDE WALL LEVEL 4.72 mPD

Drilling Progress	Casing size	Water level (m) Shift start/end	Total core Recovery %	Solid core Recovery %	R.Q.D.	Fracture Index	Tests	Samples	Reduced Level	Depth (m)	Legend	Grade	Description
21													AS SHEET 2 OF 4.
22													
23													
24													
18/07/96													
	NX 24.65m		53	0	0	NI		TNW	-19.93	24.65	+	IV	Moderately weak, brownish grey spotted yellow, highly decomposed, medium grained GRANITE with extremely closely spaced, moderately narrow to narrow, rough undulating, limonite and manganese stained joints, dipping 15°-35°.
25			100	100	100			TNW	-20.12	24.84	+	III	
26			100	100	26			TNW		25.69	+		
27			100	100	42			TNW		26.25	+		
28						9.7							Moderately strong, brownish grey spotted yellow, moderately decomposed, medium grained GRANITE with closely to extremely closely spaced, narrow to very narrow, rough undulating, limonite and manganese stained joints, dipping 5°-10° and 15°-35°.
29			100	100	66			TNW		27.78	+		
19/07/96													
29			100	100	82			TNW		29.27	+		
30										30.00	+		

- SMALL DISTURBED SAMPLE
- LARGE DISTURBED SAMPLE
- SPT LINER SAMPLE
- U76 UNDISTURBED SAMPLE
- U100 UNDISTURBED SAMPLE
- MAZIER SAMPLE (70mm)
- PISTON SAMPLE
- WATER SAMPLE
- PIEZOMETER TIP
- STANDPIPE
- STANDARD PENETRATION TEST
- PERMEABILITY TEST
- IN-SITU VANE SHEAR TEST

LOGGED BENNY WONG

DATE 20/07/96

APPROVED C.LUN

DATE 22/07/96

REMARKS



BACHY SOLETANCHE GROUP
SOIL & FOUNDATIONS SPECIALISTS

DRILLHOLE RECORD

HOLE NO. P2

CONTRACT

SHEET 4 of 4

PROJECT LINCOLN HOUSE DEVELOPMENT, QUARRY BAY

METHOD ROTARY

CO-ORDINATES

W.O. W-518

MACHINE & No. D18

E 839893.70
N 816495.10

DATE from 16/7/96 to 19/7/96

FLUSHING MEDIUM WATER

ORIENTATION Vertical

GUIDE WALL LEVEL 4.72 mPD

Drilling Progress	Casing size	Water level (m) Shift start/end	Total core Recovery %	Solid core Recovery %	R.Q.D.	Fracture Index	Tests	Samples	Reduced Level	Depth (m)	Legend	Grade	Description
19/07/96			100	100	82	9.7		TNW	-26.07	30.79	++++	III	AS SHEET 3 OF 4.
31													End of hole at 30.79m.
32													
33													
34													
35													
36													
37													
38													
39													
40													

- | | |
|---------------------------|-----------------------------|
| • SMALL DISTURBED SAMPLE | Δ WATER SAMPLE |
| ┆ LARGE DISTURBED SAMPLE | ▲ PIEZOMETER TIP |
| ▨ SPT LINER SAMPLE | ◻ STANDPIPE |
| ▨ U76 UNDISTURBED SAMPLE | ↓ STANDARD PENETRATION TEST |
| ▨ U100 UNDISTURBED SAMPLE | ┆ PERMEABILITY TEST |
| ▨ MAZIER SAMPLE (70mm) | ∇ IN-SITU VANE SHEAR TEST |
| ▨ PISTON SAMPLE | |



LOGGED BENNY WONG

DATE 20/07/96

APPROVED C.LUN

DATE 22/07/96

REMARKS

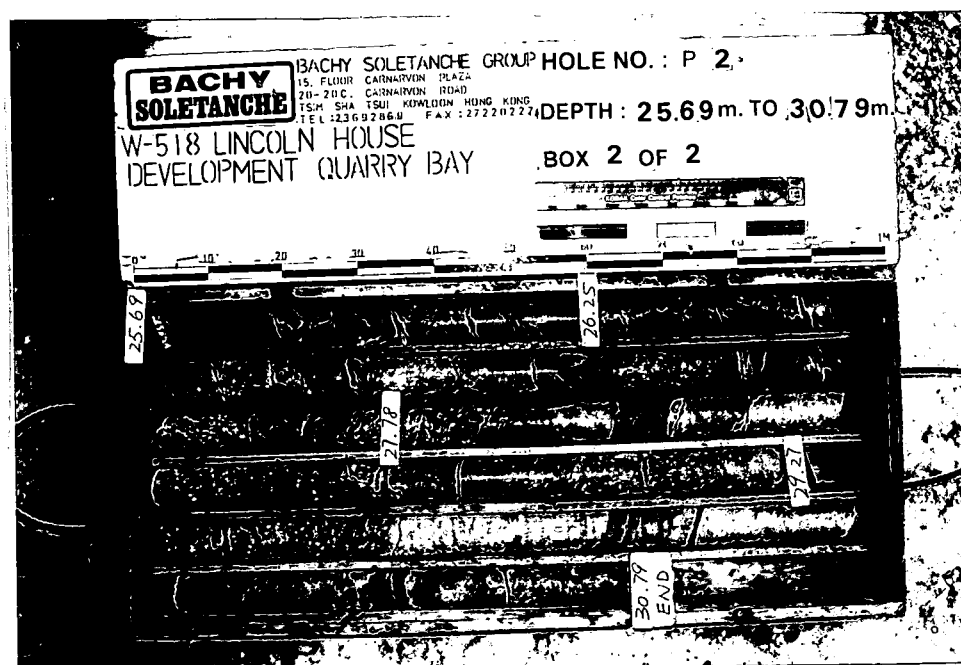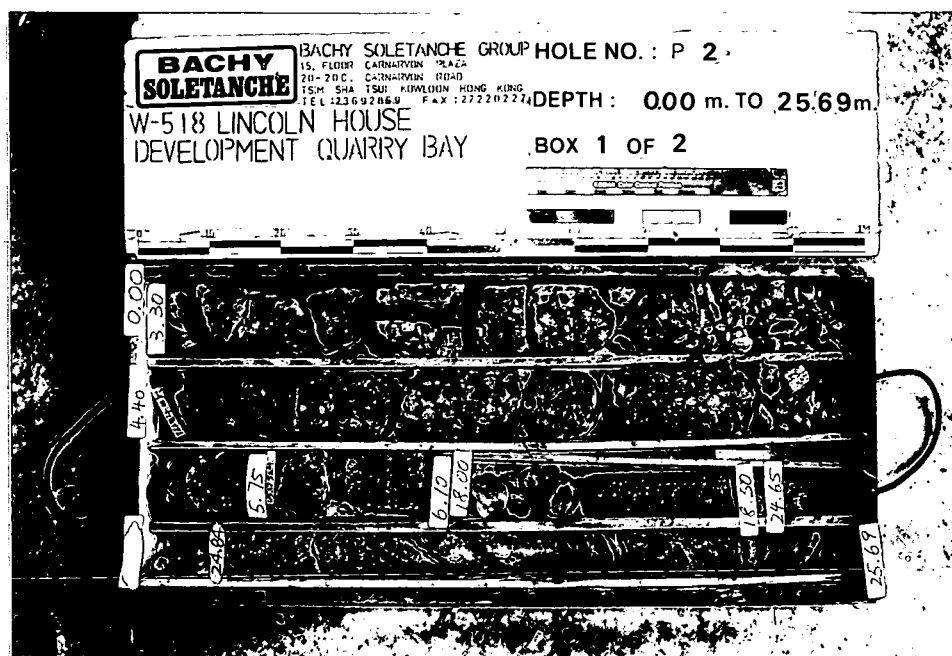



BACHY SOLETANCHE GROUP
SOIL & FOUNDATIONS SPECIALISTS

DRILLHOLE RECORD

HOLE NO. P3

SHEET 1 of 4

CONTRACT

PROJECT LINCOLN HOUSE DEVELOPMENT, QUARRY BAY

METHOD ROTARY

CO-ORDINATES

W.O. W-518

MACHINE & No. D-18

E 839893.89
N 816497.92

DATE from 19/7/96 to 21/7/96

FLUSHING MEDIUM WATER

ORIENTATION Vertical

GROUND-LEVEL 4.73 mPD

Drilling Progress	Casing size	Water level (m) Shift start/end	Total core Recovery %	Solid core Recovery %	R.Q.D.	Fracture Index	Tests	Samples	Reduced Level	Depth (m)	Legend	Grade	Description
1	PX							INSPECTION PIT					0.00m to 3.00m: wash boring/
2	PX 1.50m HX												
3			50					HX	1.73	3.00			
4									1.23	3.50			Rounded and subrounded COBBLES and fine to coarse GRAVEL and CONCRETE. No recovery assumed finer material washed out. (FILL)
5													3.50-24.30m: wash boring.
6													
7													
8													
9													
10													

- SMALL DISTURBED SAMPLE
- ▮ LARGE DISTURBED SAMPLE
- ▮ SPT LINER SAMPLE
- ▮ U76 UNDISTURBED SAMPLE
- ▮ U100 UNDISTURBED SAMPLE
- ▮ MAZIER SAMPLE (70mm)
- ▮ PISTON SAMPLE
- ▲ WATER SAMPLE
- ▲ PIEZOMETER TIP
- ▮ STANDPIPE
- ↓ STANDARD PENETRATION TEST
- ⊥ PERMEABILITY TEST
- ∇ IN-SITU VANE SHEAR TEST

LOGGED BENNY WONG

DATE 05/08/96

APPROVED C. LUN

DATE 06/08/96

REMARKS

Hole termination depth at 30.95m.



BACHY SOLETANCHE GROUP
SOIL & FOUNDATIONS SPECIALISTS

DRILLHOLE RECORD

HOLE NO. P3

SHEET 2 of 4

CONTRACT

PROJECT LINCOLN HOUSE DEVELOPMENT, QUARRY BAY

METHOD ROTARY

CO-ORDINATES

W.O. W-518

MACHINE & No. D-18

E 839893.89

DATE from 19/7/96 to 21/7/96

N 816497.92

FLUSHING MEDIUM WATER

ORIENTATION Vertical

GROUND-LEVEL 4.73 mPD

Drilling Progress	Casing size	Water level (m) Shift start/end	Total core Recovery %	Solid core Recovery %	R.Q.D.	Fracture Index	Tests	Samples	Reduced Level	Depth (m)	Legend	Grade	Description
11													AS SHEET 1 OF 4
12													
13													
14													
15													
16													
17													
18	HX 18.00m NX		60					T2-101	-13.27 -13.77	18.00 18.50			Angular COBBLES and GRAVEL, finer material washed out. (FILL)
19													
20													

- SMALL DISTURBED SAMPLE
- LARGE DISTURBED SAMPLE
- SPT LINER SAMPLE
- U76 UNDISTURBED SAMPLE
- U100 UNDISTURBED SAMPLE
- MAZIER SAMPLE (70mm)
- PISTON SAMPLE
- WATER SAMPLE
- PIEZOMETER TIP
- STANDPIPE
- STANDARD PENETRATION TEST
- PERMEABILITY TEST
- IN-SITU VANE SHEAR TEST

LOGGED BENNY WONG

DATE 05/08/96

APPROVED C. LUN

DATE 06/08/96

REMARKS



BACHY SOLETANCHE GROUP
SOIL & FOUNDATIONS SPECIALISTS

DRILLHOLE RECORD

HOLE NO. P3

SHEET 3 of 4

CONTRACT

PROJECT LINCOLN HOUSE DEVELOPMENT, QUARRY BAY

METHOD ROTARY

CO-ORDINATES

W.O. W-518

MACHINE & No. D-18

E 839893.89

N 816497.92

DATE from 19/7/96 to 21/7/96

FLUSHING MEDIUM WATER

ORIENTATION Vertical

GROUND-LEVEL 4.73 mPD

Drilling Progress	Casing size	Water level (m) Shift start/end	Total core Recovery %	Solid core Recovery %	R.Q.D.	Fracture Index	Tests	Samples	Reduced Level	Depth (m)	Legend	Grade	Description
21													AS SHEET 2 OF 4
22													
23													
24	NX 24.30m												
25			50	0	0	NI		TNW	-19.57	24.30			
26			100	100	43			TNW		24.50	+	III	Moderately strong, brownish grey grey, spotted yellow, moderately decomposed, medium grained GRANITE with closely to extremely closely spaced, rough, undulating, narrow to very narrow, limonite and manganese stained joints, dipping 5° to 15° and 15° to 35°.
27			99	99	49	11.1		TNW		25.25	+		
28			98	94	41			TNW		26.81	+		
29			100	100	48			TNW		26.81	+		
30			99	99	57	5.1		TNW	-24.01	28.03	+	III/II	Moderately strong to strong, brownish grey, spotted yellow, moderately to slightly decomposed, medium grained GRANITE with closely spaced, rough, undulating, narrow, limonite and manganese

- SMALL DISTURBED SAMPLE
- LARGE DISTURBED SAMPLE
- SPT LINER SAMPLE
- U76 UNDISTURBED SAMPLE
- U100 UNDISTURBED SAMPLE
- MAZIER SAMPLE (70mm)
- PISTON SAMPLE
- WATER SAMPLE
- PIEZOMETER TIP
- STANDPIPE
- STANDARD PENETRATION TEST
- PERMEABILITY TEST
- IN-SITU VANE SHEAR TEST

LOGGED BENNY WONG

DATE 05/08/96

APPROVED C. LUN

DATE 06/08/96

REMARKS



BACHY SOLETANCHE GROUP
SOIL & FOUNDATIONS SPECIALISTS

DRILLHOLE RECORD

HOLE NO. P3

SHEET 4 of 4

CONTRACT

PROJECT LINCOLN HOUSE DEVELOPMENT, QUARRY BAY

METHOD ROTARY

CO-ORDINATES

W.O. W-518

MACHINE & No. D-18

E 839893.89
N 816497.92

DATE from 19/7/96 to 21/7/96

FLUSHING MEDIUM WATER

ORIENTATION Vertical

GROUND-LEVEL 4.73 mPD

Drilling Progress	Casing size	Water level (m) Shift start/end	Total core Recovery %	Solid core Recovery %	R.Q.D.	Fracture Index	Tests	Samples	Reduced Level	Depth (m)	Legend	Grade	Description
21/07/96			100	100	80			↑ TN ↓	-26.22	30.95	++++ ++++ ++++ ++++		stained, dipping 5° to 10°.
31													End of hole at 30.95m.
32													
33													
34													
35													
36													
37													
38													
39													
40													

- SMALL DISTURBED SAMPLE
- ▬ LARGE DISTURBED SAMPLE
- ▨ SPT LINER SAMPLE
- ▩ U76 UNDISTURBED SAMPLE
- ▩ U100 UNDISTURBED SAMPLE
- ▩ MAZIER SAMPLE (70mm)
- ▩ PISTON SAMPLE
- △ WATER SAMPLE
- ▲ PIEZOMETER TIP
- STANDPIPE
- ⊥ STANDARD PENETRATION TEST
- ⊥ PERMEABILITY TEST
- √ IN-SITU VANE SHEAR TEST



LOGGED BENNY WONG

DATE 05/08/96

APPROVED C. LUN

DATE 06/08/96

REMARKS

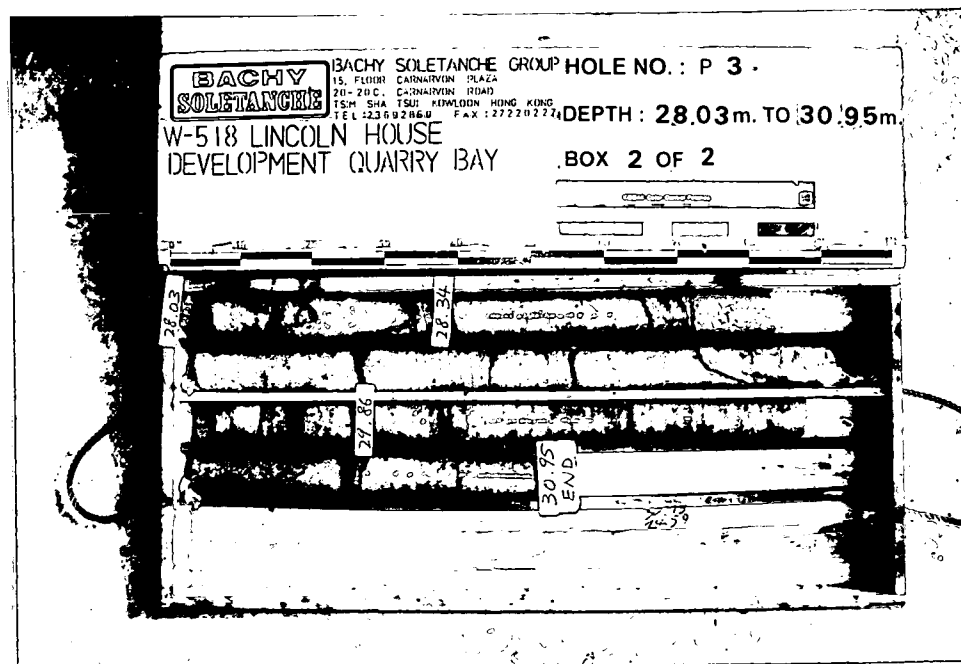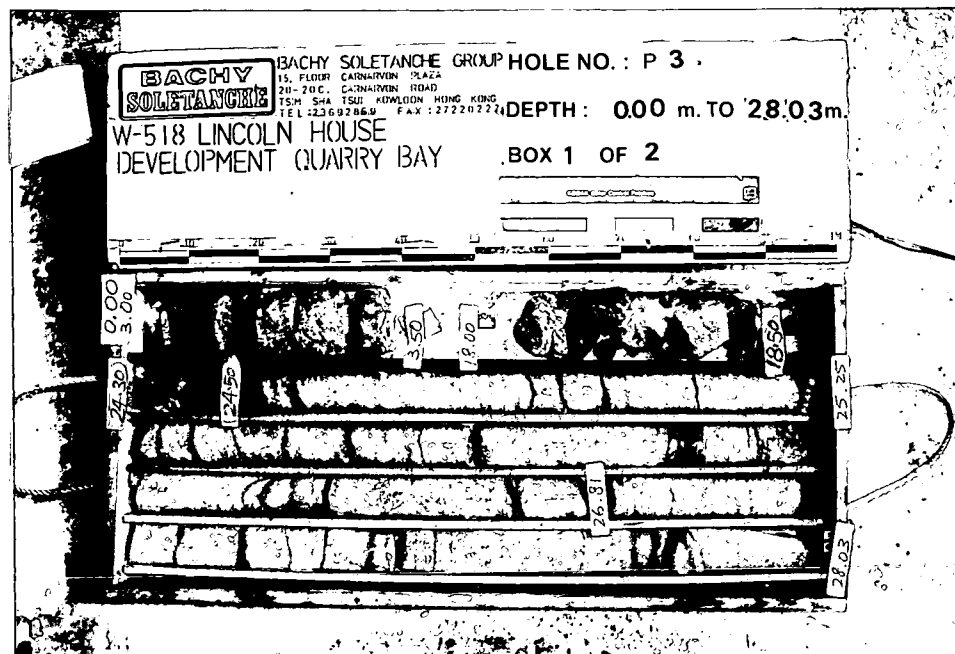



BACHY SOLETANCHE GROUP
SOIL & FOUNDATIONS SPECIALISTS

DRILLHOLE RECORD

HOLE NO. P4

SHEET 1 of 4

CONTRACT

PROJECT LINCOLN HOUSE DEVELOPMENT, QUARRY BAY

METHOD ROTARY

CO-ORDINATES

W.O. W-518

MACHINE & No. D-12

E 839894.00
N 816500.44

DATE from 15/7/96 to 17/7/96

FLUSHING MEDIUM WATER

ORIENTATION Vertical

GROUND-LEVEL 4.73 mPD

Drilling Progress	Casing size	Water level (m) Shift start/end	Total core Recovery %	Solid core Recovery %	R.Q.D.	Fracture Index	Tests	Samples	Reduced Level	Depth (m)	Legend	Grade	Description
1	PX							INSPECTION PIT					0.00-2.80m: wash boring
2													
3	PX 2.80m HX		80					HX	1.93 2.80 1.43 3.30				Rounded and subrounded COBBLES and fine to coarse GRAVEL, CONCRETE. No recovery assumed finer material washed out. 3.30-19.17m: wash boring
4													
5													
6													
7													
8	HX 8.00m NX												
9													
10													

- SMALL DISTURBED SAMPLE
- LARGE DISTURBED SAMPLE
- SPT LINER SAMPLE
- U76 UNDISTURBED SAMPLE
- U100 UNDISTURBED SAMPLE
- MAZIER SAMPLE (70mm)
- PISTON SAMPLE
- WATER SAMPLE
- PIEZOMETER TIP
- STANDPIPE
- STANDARD PENETRATION TEST
- PERMEABILITY TEST
- IN-SITU VANE SHEAR TEST

LOGGED BENNY WONG

DATE 23/07/96

APPROVED C. LUN

DATE 25/07/96

REMARKS

Hole termination depth at 28.92m.
0.00-2.00m: Inspection pit



BACHY SOLETANCHE GROUP
SOIL & FOUNDATIONS SPECIALISTS

DRILLHOLE RECORD

HOLE NO. P4

CONTRACT

SHEET 2 of 4

PROJECT LINCOLN HOUSE DEVELOPMENT, QUARRY BAY

METHOD ROTARY

CO-ORDINATES

W.O. W-518

MACHINE & No. D-12

E 839894.00
N 816500.44

DATE from 15/7/96 to 17/7/96

FLUSHING MEDIUM WATER

ORIENTATION Vertical

GROUND-LEVEL 4.73 mPD

Drilling Progress	Casing size	Water level (m) Shift start/end	Total core Recovery %	Solid core Recovery %	R.Q.D.	Fracture Index	Tests	Samples	Reduced Level	Depth (m)	Legend	Grade	Description
11													
12													
13													
14													
15													
16													
17													
18													
19			59						-14.44 -14.57	19.17 19.30			
20													Rounded to subrounded COBBLES and fine to coarse GRAVEL. No recovery assumed finer material washed out.

- SMALL DISTURBED SAMPLE
- ▬ LARGE DISTURBED SAMPLE
- ▬ SPT LINER SAMPLE
- ▬ U76 UNDISTURBED SAMPLE
- ▬ U100 UNDISTURBED SAMPLE
- ▬ MAZIER SAMPLE (70mm)
- ▬ PISTON SAMPLE
- Δ WATER SAMPLE
- ▲ PIEZOMETER TIP
- STANDPIPE
- ↓ STANDARD PENETRATION TEST
- ⊥ PERMEABILITY TEST
- ∨ IN-SITU VANE SHEAR TEST

LOGGED BENNY WONG

DATE 23/07/96

APPROVED C. LUN

DATE 25/07/96

REMARKS



BACHY SOLETANCHE GROUP
SOIL & FOUNDATIONS SPECIALISTS

DRILLHOLE RECORD

HOLE NO. P4

SHEET 3 of 4

CONTRACT

PROJECT LINCOLN HOUSE DEVELOPMENT, QUARRY BAY

METHOD ROTARY

CO-ORDINATES

W.O. W-518

MACHINE & No. D-12

E 839894.00

DATE from 15/7/96 to 17/7/96

N 816500.44

FLUSHING MEDIUM WATER

ORIENTATION Vertical

GROUND-LEVEL 4.73 mPD

Drilling Progress	Casing size	Water level (m) Shift start/end	Total core Recovery %	Solid core Recovery %	R.Q.D.	Fracture Index	Tests	Samples	Reduced Level	Depth (m)	Legend	Grade	Description
21													19.30-23.40m: wash boring
22													
23													
24													
25													
26													
27													
28													
29													
30													

SMALL DISTURBED SAMPLE	WATER SAMPLE
LARGE DISTURBED SAMPLE	PIEZOMETER TIP
SPT LINER SAMPLE	STANDPIPE
U76 UNDISTURBED SAMPLE	STANDARD PENETRATION TEST
U100 UNDISTURBED SAMPLE	PERMEABILITY TEST
MAZIER SAMPLE (70mm)	IN-SITU VANE SHEAR TEST
PISTON SAMPLE	

LOGGED BENNY WONG

DATE 23/07/96

APPROVED C. LUN

DATE 25/07/96

REMARKS

Rounded and subrounded COBBLES and fine to coarse GRAVEL. No recovery assumed finer material washed out.

Moderately weak, brownish grey, spotted black and yellow, moderately to highly decomposed, medium grained GRANITE with closely spaced, narrow to very narrow, rough undulating, limonite and manganese stained joints, dipping 15° to 35°.

Moderately weak, brownish grey, spotted black, moderately to highly decomposed, medium grained GRANITE with extremely closely to closely spaced, moderately narrow to narrow, rough stepped, limonite and manganese stained joints, dipping 15° to 35°.

Moderately strong to strong, brownish and pinkish grey, spotted black and white, moderately to slightly decomposed, medium grained GRANITE with closely to medium spaced, very narrow to extremely narrow, limonite stained joints, dipping 5° to 15°.

Strong, pinkish grey, spotted black and white, slightly decomposed, medium grained GRANITE with medium spaced, extremely narrow,



BACHY SOLETANCHE GROUP
SOIL & FOUNDATIONS SPECIALISTS

DRILLHOLE RECORD

HOLE NO. P4

CONTRACT

SHEET 4 of 4

PROJECT LINCOLN HOUSE DEVELOPMENT, QUARRY BAY

METHOD ROTARY

CO-ORDINATES

W.O. W-518

MACHINE & No. D-12

E 839894.00
N 816500.44

DATE from 15/7/96 to 17/7/96

FLUSHING MEDIUM WATER

ORIENTATION Vertical

GROUND-LEVEL 4.73 mPD

Drilling Progress	Casing size	Water level (m) Shift start/end	Total core Recovery %	Solid core Recovery %	R.Q.D.	Fracture Index	Tests	Samples	Reduced Level	Depth (m)	Legend	Grade	Description
31													clean joints, dipping 5° to 10°. End of hole at 28.92m.
32													
33													
34													
35													
36													
37													
38													
39													
40													

- SMALL DISTURBED SAMPLE
- ▬ LARGE DISTURBED SAMPLE
- ▨ SPT LINER SAMPLE
- ▩ U76 UNDISTURBED SAMPLE
- ▩ U100 UNDISTURBED SAMPLE
- ▩ MAZIER SAMPLE (70mm)
- ▩ PISTON SAMPLE
- Δ WATER SAMPLE
- ▲ PIEZOMETER TIP
- STANDPIPE
- ⊥ STANDARD PENETRATION TEST
- ⊥ PERMEABILITY TEST
- ∇ IN-SITU VANE SHEAR TEST



LOGGED BENNY WONG

DATE 23/07/96

APPROVED C. LUN

DATE 25/07/96

REMARKS

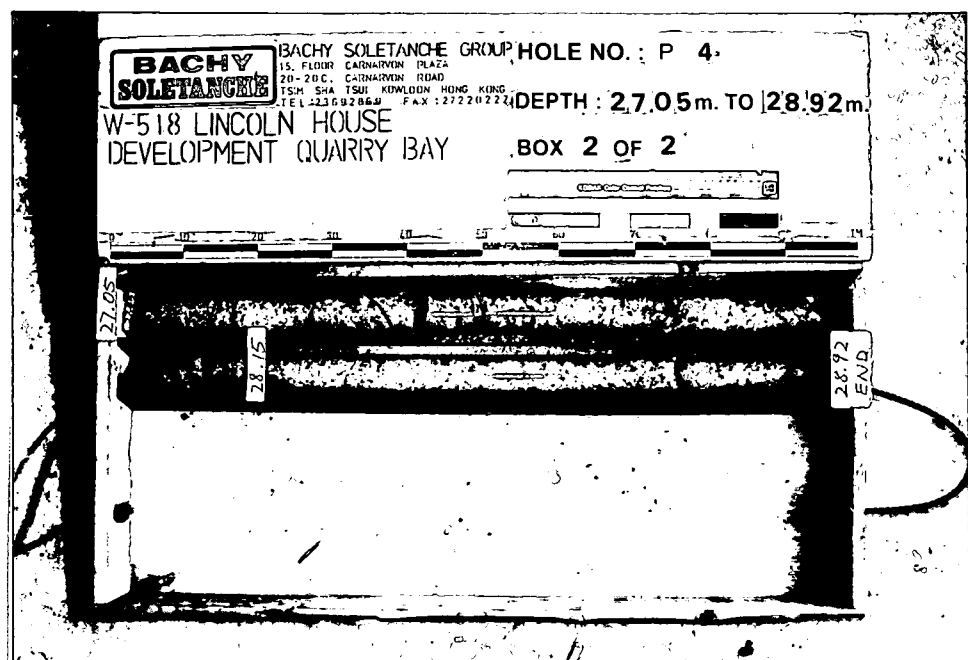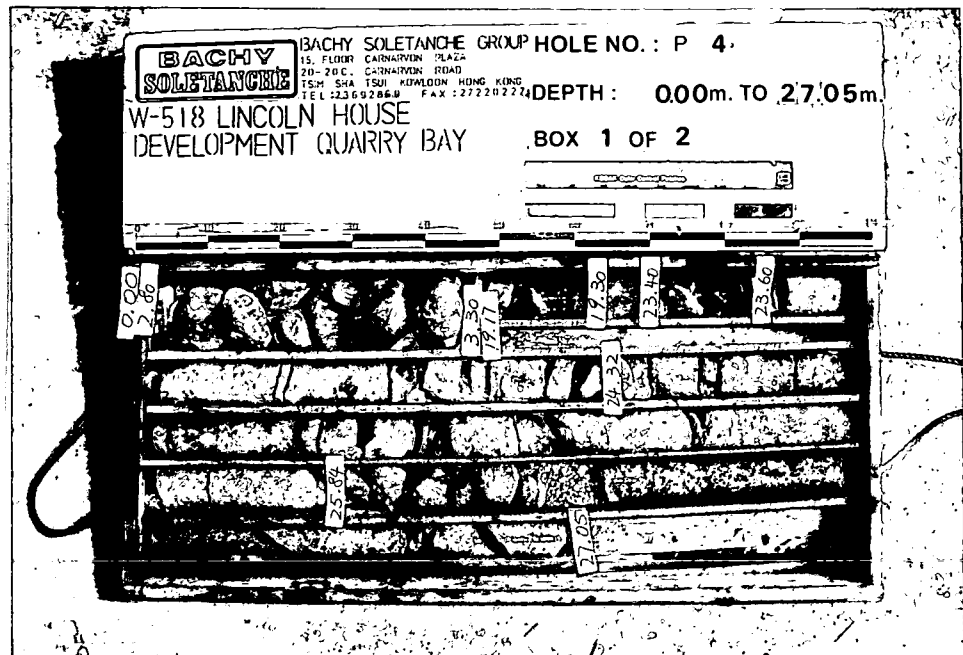



BACHY SOLETANCHE GROUP
SOIL & FOUNDATIONS SPECIALISTS

DRILLHOLE RECORD

HOLE NO. P61

CONTRACT

SHEET 1 of 3

PROJECT LINCOLN HOUSE DEVELOPMENT, QUARRY BAY

METHOD ROTARY

CO-ORDINATES

W.O. W-518

MACHINE & No. D-12

E 839928.33

N 816500.02

DATE from 20/7/96 to 23/7/96

FLUSHING MEDIUM WATER

ORIENTATION Vertical

GUIDE WALL LEVEL 4.49 mPD

Drilling Progress	Casing size	Water level (m) Shift start/end	Total core Recovery %	Solid core Recovery %	R.Q.D.	Fracture Index	Tests	Samples	Reduced Level	Depth (m)	Legend	Grade	Description
1 20/07/96	PX								2.89	1.60			Wash boring.
2	PX 2.36m HX		80						2.79	1.70			Concrete Wash boring.
3			44						2.29	2.20			Concrete Wash boring.
4									2.13	2.36			
5													
6 21/07/96													
7													
8													
9													
10													

- SMALL DISTURBED SAMPLE
- LARGE DISTURBED SAMPLE
- SPT LINER SAMPLE
- U76 UNDISTURBED SAMPLE
- U100 UNDISTURBED SAMPLE
- MAZIER SAMPLE (70mm)
- PISTON SAMPLE
- WATER SAMPLE
- PIEZOMETER TIP
- STANDPIPE
- STANDARD PENETRATION TEST
- PERMEABILITY TEST
- IN-SITU VANE SHEAR TEST

LOGGED BENNY WONG

DATE 24/07/96

APPROVED C.LUN

DATE 25/07/96

REMARKS
Hole termination depth at 25.80m.



BACHY SOLETANCHE GROUP
SOIL & FOUNDATIONS SPECIALISTS

DRILLHOLE RECORD

HOLE NO. P61

CONTRACT

SHEET 2 of 3

PROJECT LINCOLN HOUSE DEVELOPMENT, QUARRY BAY

METHOD ROTARY

CO-ORDINATES

W.O. W-518

MACHINE & No. D-12

E 839928.33

N 816500.02

DATE from 20/7/96 to 23/7/96

FLUSHING MEDIUM WATER

ORIENTATION Vertical

GUIDE WALL LEVEL 4.49 mPD

Drilling Progress	Casing size	Water level (m) Shift start/end	Total core Recovery %	Solid core Recovery %	R.Q.D.	Fracture Index	Tests	Samples	Reduced Level	Depth (m)	Legend	Grade	Description
11													AS SHEET 1 OF 3.
12	HX 12.00m NX												
13													
14													
15													
16													
17													
18	NX 17.57m												
19			100	100	100								
20			100	100	100	3.7							
21													Strong, pinkish grey, spotted black and white, slightly decomposed, medium grained GRANITE, with closely to medium spaced, very narrow to extremely narrow, rough undulating, limonite and stained joints, dipping 5°-10°.
22													

- SMALL DISTURBED SAMPLE
- LARGE DISTURBED SAMPLE
- ▨ SPT LINER SAMPLE
- ▨ U76 UNDISTURBED SAMPLE
- ▨ U100 UNDISTURBED SAMPLE
- ▨ MAZIER SAMPLE (70mm)
- ▨ PISTON SAMPLE
- △ WATER SAMPLE
- ▲ PIEZOMETER TIP
- △ STANDPIPE
- ↓ STANDARD PENETRATION TEST
- ⊥ PERMEABILITY TEST
- ∇ IN-SITU VANE SHEAR TEST

LOGGED BENNY WONG

DATE 24/07/96

APPROVED C.LUN

DATE 25/07/96

REMARKS



BACHY SOLETANCHE GROUP
SOIL & FOUNDATIONS SPECIALISTS

DRILLHOLE RECORD

HOLE NO. P61

CONTRACT

SHEET 3 of 3

PROJECT LINCOLN HOUSE DEVELOPMENT, QUARRY BAY

METHOD ROTARY

CO-ORDINATES

W.O. W-518

MACHINE & No. D-12

E 839928.33
N 816500.02

DATE from 20/7/96 to 23/7/96

FLUSHING MEDIUM WATER

ORIENTATION Vertical



GUIDE WALL LEVEL 4.49 mPD

Drilling Progress	Casing size	Water level (m) Shift start/end	Total core Recovery %	Solid core Recovery %	R.Q.D.	Fracture Index	Tests	Samples	Reduced Level	Depth (m)	Legend	Grade	Description
21			100	100	100			T2 -101		20.56	++	II	AS SHEET 2 OF 3.
22			100	100	100			T2 -101		21.79	++		
23			100	100	100	3.7		T2 -101		22.89	++		
24			100	100	100			T2 -101		23.91	++		
25			100	100	100			T2 -101	-20.21	24.70	++		
25.80			100	100	90	5.5		T2 -101	-21.31	25.80	++	II/III	24.70m-25.80m: strong to moderately strong, slightly to moderately decomposed zone.
26													End of hole at 25.80m.
27													
28													
29													
30													

- SMALL DISTURBED SAMPLE
- LARGE DISTURBED SAMPLE
- SPT LINER SAMPLE
- U76 UNDISTURBED SAMPLE
- U100 UNDISTURBED SAMPLE
- MAZIER SAMPLE (70mm)
- PISTON SAMPLE
- WATER SAMPLE
- PIEZOMETER TIP
- STANDPIPE
- STANDARD PENETRATION TEST
- PERMEABILITY TEST
- IN-SITU VANE SHEAR TEST

LOGGED BENNY WONG
DATE 24/07/96
APPROVED C.LUN
DATE 25/07/96

REMARKS

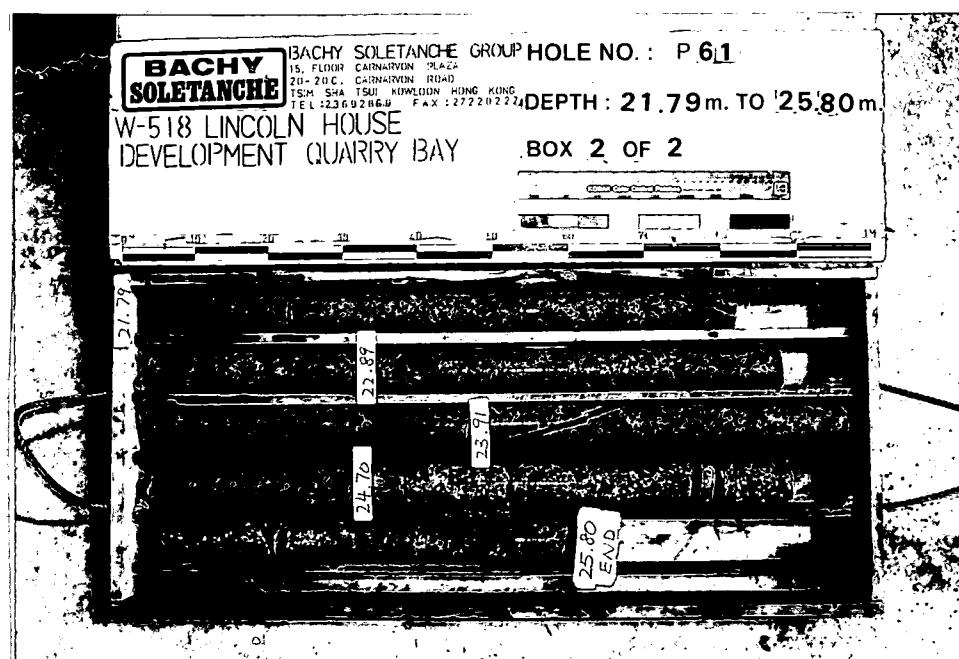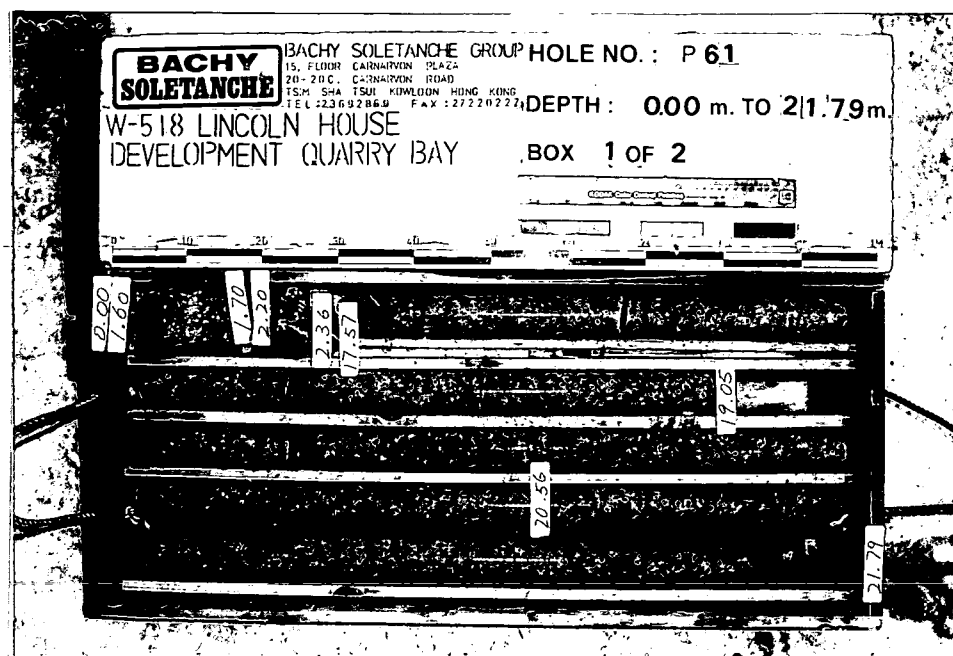



BACHY SOLETANCHE GROUP
SOIL & FOUNDATIONS SPECIALISTS

DRILLHOLE RECORD

HOLE NO. P62

CONTRACT

SHEET 1 of 3

PROJECT LINCOLN HOUSE DEVELOPMENT, QUARRY BAY

METHOD ROTARY

CO-ORDINATES

W.O. W-518

MACHINE & No. D-16

E 839928.24

N 816496.80

DATE from 19/7/96 to 19/7/96

FLUSHING MEDIUM WATER

ORIENTATION Vertical

GUIDE WALL LEVEL 4.49 mPD

Drilling Progress	Casing size	Water level (m) Shift start/end	Total core Recovery %	Solid core Recovery %	R.Q.D.	Fracture Index	Tests	Samples	Reduced Level	Depth (m)	Legend	Grade	Description
1	NX												0.00-3.00m: wash boring
2													
3			70					HX	1.49	3.00			
4									0.99	3.50			Rounded and subrounded COBBLES and fine to coarse GRAVEL and CONCRETE. No recovery assumed finer material was out. 3.50-17.37m: wash boring
5													
6													
7													
8													
9													
10													

- SMALL DISTURBED SAMPLE
- LARGE DISTURBED SAMPLE
- SPT LINER SAMPLE
- U76 UNDISTURBED SAMPLE
- U100 UNDISTURBED SAMPLE
- MAZIER SAMPLE (70mm)
- PISTON SAMPLE
- WATER SAMPLE
- PIEZOMETER TIP
- STANDPIPE
- STANDARD PENETRATION TEST
- PERMEABILITY TEST
- IN-SITU VANE SHEAR TEST

LOGGED BENNY WONG

DATE 30/0796

APPROVED C. LUN

DATE 31/07/96

REMARKS
Hole termination depth at 24.91m.



BACHY SOLETANCHE GROUP
SOIL & FOUNDATIONS SPECIALISTS

DRILLHOLE RECORD

HOLE NO. P62

CONTRACT

SHEET 2 of 3

PROJECT LINCOLN HOUSE DEVELOPMENT, QUARRY BAY

METHOD ROTARY

CO-ORDINATES

W.O. W-518

MACHINE & No. D-16

E 839928.24
N 816496.80

DATE from 19/7/96 to 19/7/96

FLUSHING MEDIUM WATER

ORIENTATION Vertical

GUIDE WALL LEVEL 4.49 mPD

Drilling Progress	Casing size	Water level (m) Shift start/end	Total core Recovery %	Solid core Recovery %	R.Q.D.	Fracture Index	Tests	Samples	Reduced Level	Depth (m)	Legend	Grade	Description
11													AS SHEET 1 OF 3
12													
13													
14													
15													
16													Strong, pinkish grey, spotted black and white, slightly decomposed, medium grained GRANITE with closely to medium spaced, very narrow to extremely narrow, rough, undulating, clean joints, dipping 5° to 10°.
17	HX 17.37m NX								-12.88	17.37			
18			98	98	98			TNW		17.97		II	
19			99	99	97			TNW		18.95			
20			100	100	100			TNW					

- SMALL DISTURBED SAMPLE
- ▬ LARGE DISTURBED SAMPLE
- ▨ SPT LINER SAMPLE
- ▩ U76 UNDISTURBED SAMPLE
- ▩ U100 UNDISTURBED SAMPLE
- ▨ MAZIER SAMPLE (70mm)
- ▩ PISTON SAMPLE
- △ WATER SAMPLE
- ▲ PIEZOMETER TIP
- STANDPIPE
- ⊥ STANDARD PENETRATION TEST
- ⊥ PERMEABILITY TEST
- √ IN-SITU VANE SHEAR TEST

LOGGED BENNY WONG
DATE 30/0796
APPROVED C. LUN
DATE 31/07/96

REMARKS



BACHY SOLETANCHE GROUP
SOIL & FOUNDATIONS SPECIALISTS

DRILLHOLE RECORD

HOLE NO. P62

CONTRACT

SHEET 3 of 3

PROJECT LINCOLN HOUSE DEVELOPMENT, QUARRY BAY

METHOD ROTARY

CO-ORDINATES

W.O. W-518

MACHINE & No. D-16

E 839928.24

DATE from 19/7/96 to 19/7/96

N 816496.80

FLUSHING MEDIUM WATER

ORIENTATION Vertical

GUIDE WALL LEVEL 4.49 mPD

Drilling Progress	Casing size	Water level (m) Shift start/end	Total core Recovery %	Solid core Recovery %	R.Q.D.	Fracture Index	Tests	Samples	Reduced Level	Depth (m)	Legend	Grade	Description
21 19/07/96			100	100	95			TNW		20.04	+		AS SHEET 2 OF 3
22			100	100	100			TNW		21.44	+		
23			99	94	86			TNW		22.98	+		
24			99	99	94			TNW		23.95	+		
25									-20.42	24.91	+		
26													End of hole at 24.91m.
27													
28													
29													
30													

- ▲ SMALL DISTURBED SAMPLE
- ▲ LARGE DISTURBED SAMPLE
- ▨ SPT LINER SAMPLE
- ▨ U76 UNDISTURBED SAMPLE
- ▨ U100 UNDISTURBED SAMPLE
- ▨ MAZIER SAMPLE (70mm)
- ▨ PISTON SAMPLE
- ▲ WATER SAMPLE
- ▲ PIEZOMETER TIP
- ▨ STANDPIPE
- ▨ STANDARD PENETRATION TEST
- ▨ PERMEABILITY TEST
- ▨ IN-SITU VANE SHEAR TEST



LOGGED BENNY WONG

DATE 30/07/96

APPROVED C. LUN

DATE 31/07/96

REMARKS

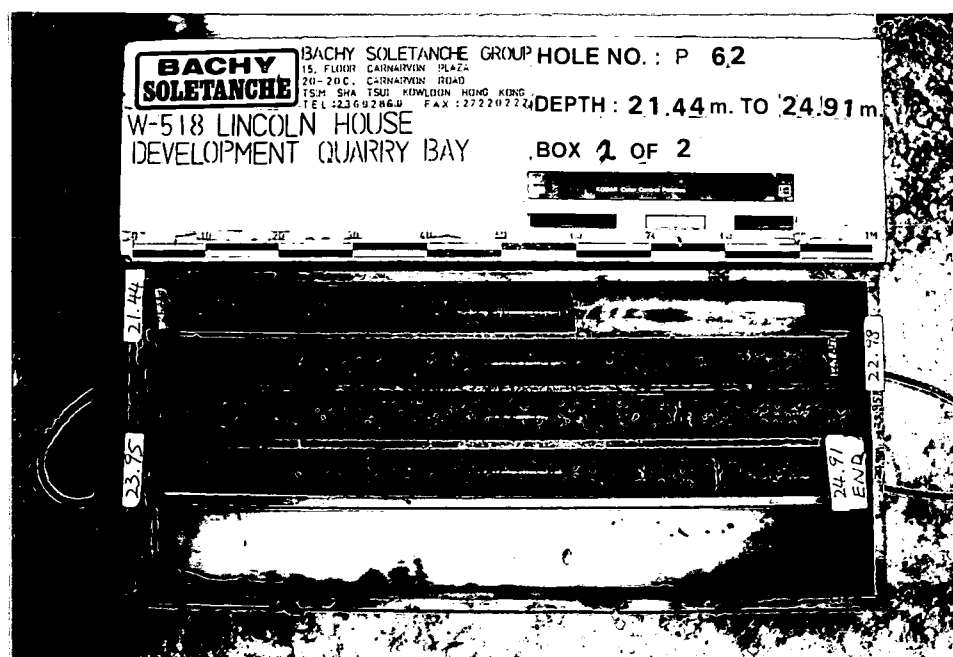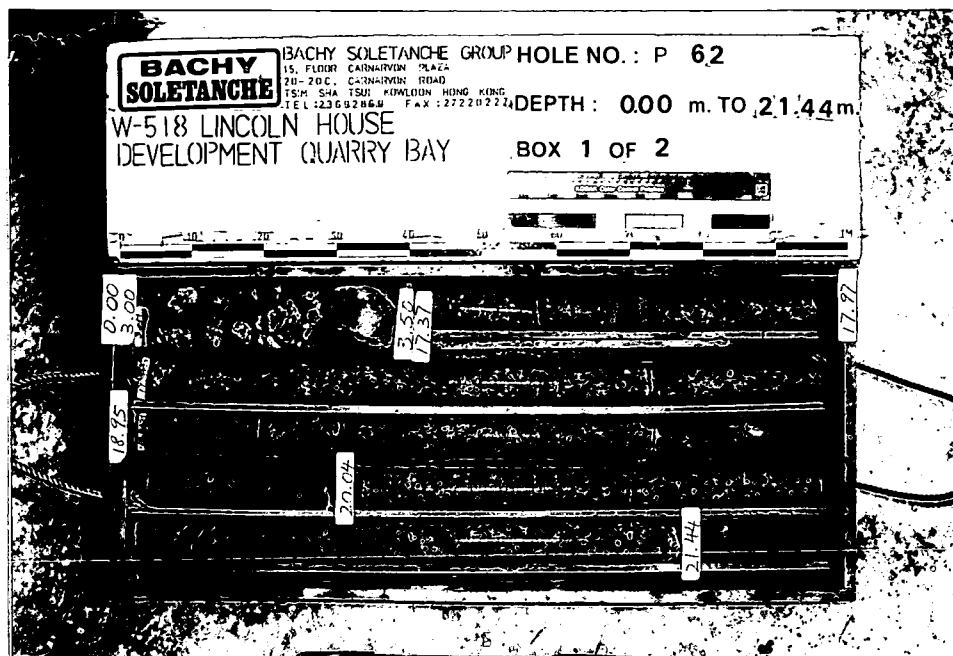



BACHY SOLETANCHE GROUP
SOIL & FOUNDATIONS SPECIALISTS

DRILLHOLE RECORD

HOLE NO. P63

CONTRACT

SHEET 1 of 3

PROJECT LINCOLN HOUSE DEVELOPMENT, QUARRY BAY

METHOD ROTARY

CO-ORDINATES

W.O. W-518

MACHINE & No. D-17

E 839928.16
N 816493.66

DATE from 19/7/96 to 20/7/96

FLUSHING MEDIUM WATER

ORIENTATION Vertical

GROUND-LEVEL 4.50 mPD

Drilling Progress	Casing size	Water level (m) Shift start/end	Total core Recovery %	Solid core Recovery %	R.Q.D.	Fracture Index	Tests	Samples	Reduced Level	Depth (m)	Legend	Grade	Description
1	PX							INSPECTION PIT					0.00-2.00m: wash boring
2	PX 2.00m HX		45					HX	2.50	2.00			Rounded to subrounded COBBLES and fine to coarse GRAVEL and CONCRETE. No recovery assumed, finer material washed out. (FILL)
3			100					HX	1.00	3.00			
4										3.50			3.50-17.55m: wash boring
5													
6													
7													
8													
9													
10													

- SMALL DISTURBED SAMPLE
- ▬ LARGE DISTURBED SAMPLE
- ▨ SPT LIVER SAMPLE
- ▩ U76 UNDISTURBED SAMPLE
- ▩ U100 UNDISTURBED SAMPLE
- ▨ MAZIER SAMPLE (70mm)
- ▩ PISTON SAMPLE
- △ WATER SAMPLE
- ▲ PIEZOMETER TIP
- STANDPIPE
- ⊥ STANDARD PENETRATION TEST
- ⊥ PERMEABILITY TEST
- ∇ IN-SITU VANE SHEAR TEST

LOGGED BENNY WONG

DATE 05/08/96

APPROVED C. LUN

DATE 06/08/96

REMARKS

Hole termination depth at 25.25m.
Inspection pit at 0.00m to 2.00m.



BACHY SOLETANCHE GROUP
SOIL & FOUNDATIONS SPECIALISTS

DRILLHOLE RECORD

HOLE NO. P63

CONTRACT

SHEET 2 of 3

PROJECT LINCOLN HOUSE DEVELOPMENT, QUARRY BAY

METHOD ROTARY

CO-ORDINATES

W.O. W-518

MACHINE & No. D-17

E 839928.16
N 816493.66

DATE from 19/7/96 to 20/7/96

FLUSHING MEDIUM WATER

ORIENTATION Vertical

GROUND-LEVEL 4.50 mPD

Drilling Progress	Casing size	Water level (m) Shift start/end	Total core Recovery %	Solid core Recovery %	R.Q.D.	Fracture Index	Tests	Samples	Reduced Level	Depth (m)	Legend	Grade	Description
11													
12													
13													
14													
15	HX 15.00m NX												
16													
17	NX 17.55m												
18			99	99	99		TNW		-13.05	17.55	+	III	Moderately strong, brownish grey, spotted yellow, moderately decomposed, medium grained GRANITE with closely to extremely closely spaced, moderately narrow to narrow, rough undulating, limonite and manganese stained joints, dipping 15° to 35° and occasional subvertical.
19						7.6				19.05	+		
20			100	100	36		TNW				+		

- SMALL DISTURBED SAMPLE
- ▬ LARGE DISTURBED SAMPLE
- ▨ SPT LINER SAMPLE
- ▩ U76 UNDISTURBED SAMPLE
- ▩ U100 UNDISTURBED SAMPLE
- ▨ MAZIER SAMPLE (70mm)
- ▩ PISTON SAMPLE
- ▲ WATER SAMPLE
- ▲ PIEZOMETER TIP
- ▢ STANDPIPE
- ↓ STANDARD PENETRATION TEST
- ⊥ PERMEABILITY TEST
- ∇ IN-SITU VANE SHEAR TEST

LOGGED BENNY WONG

DATE 05/08/96

APPROVED C. LUN

DATE 06/08/96

REMARKS



BACHY SOLETANCHE GROUP
SOIL & FOUNDATIONS SPECIALISTS

DRILLHOLE RECORD

HOLE NO. P63

SHEET 3 of 3

CONTRACT

PROJECT LINCOLN HOUSE DEVELOPMENT, QUARRY BAY

METHOD ROTARY

CO-ORDINATES

W.O. W-518

MACHINE & No. D-17

E 839928.16

DATE from 19/7/96 to 20/7/96

N 816493.66

FLUSHING MEDIUM WATER

ORIENTATION Vertical

GROUND-LEVEL 4.50 mPD

Drilling Progress	Casing size	Water level (m) Shift start/end	Total core Recovery %	Solid core Recovery %	R.Q.D.	Fracture Index	Tests	Samples	Reduced Level	Depth (m)	Legend	Grade	Description
21			100	100	100			TNW	-15.80	20.30	+++	III/II	Strong to moderately strong, pinkish grey, spotted black and white, slightly to moderately decomposed, medium grained GRANITE with closely to medium spaced, very narrow to extremely narrow, rough undulating, limonite stained joints, dipping 5° to 10°.
			100	100	100			TNW		21.26	+++		
22			100	100	100			TNW		21.80	+++		
			100	100	100			TNW		22.90	+++		
23			100	100	100			TNW		24.32	+++		
24			100	100	100			TNW		25.25	+++		
25			100	100	100			TNW	-20.75	25.25	+++		End of hole at 25.25m.
26													
27													
28													
29													
30													

- SMALL DISTURBED SAMPLE
- LARGE DISTURBED SAMPLE
- SPT LINER SAMPLE
- U76 UNDISTURBED SAMPLE
- U100 UNDISTURBED SAMPLE
- MAZIER SAMPLE (70mm)
- PISTON SAMPLE
- WATER SAMPLE
- PIEZOMETER TIP
- STANDPIPE
- STANDARD PENETRATION TEST
- PERMEABILITY TEST
- IN-SITU VANE SHEAR TEST



LOGGED BENNY WONG

DATE 05/08/96

APPROVED C. LUN

DATE 06/08/96

REMARKS

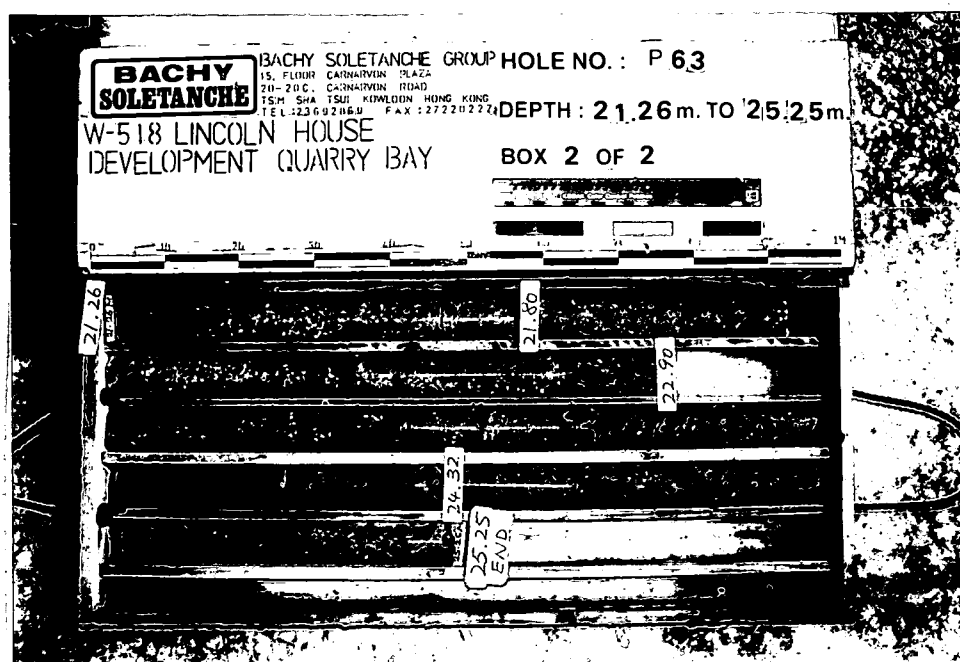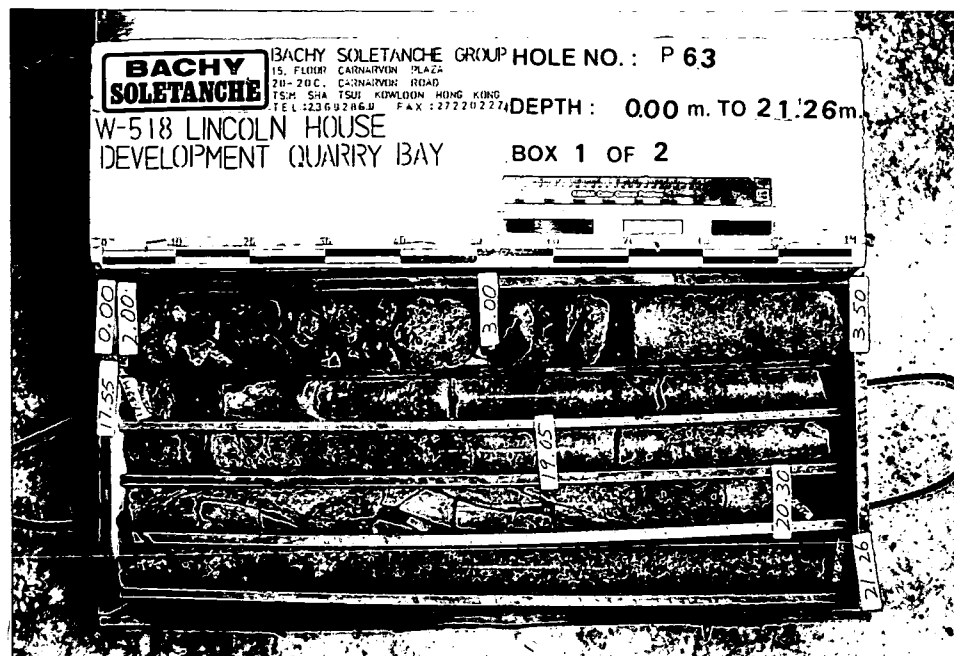



BACHY SOLETANCHE GROUP
SOIL & FOUNDATIONS SPECIALISTS

DRILLHOLE RECORD

HOLE NO. P64

SHEET 1 of 3

CONTRACT

PROJECT LINCOLN HOUSE DEVELOPMENT, QUARRY BAY

METHOD ROTARY

CO-ORDINATES

W.O. W-518

MACHINE & No. D-17

E 839928.08
N 816490.56

DATE from 17/7/96 to 18/7/96

FLUSHING MEDIUM WATER

ORIENTATION Vertical

GROUND-LEVEL 4.54 mPD

Drilling Progress	Casing size	Water level (m) Shift start/end	Total core Recovery %	Solid core Recovery %	R.Q.D.	Fracture Index	Tests	Samples	Reduced Level	Depth (m)	Legend	Grade	Description
1 17/07/96	PX							INSPECTION PIT					0.00-2.00m: wash boring
2									2.54	2.00			
3	PX 3.00m HX		60					PX	1.54	3.00			Rounded to subrounded COBBLES and fine to coarse GRAVEL. No recovery assumed, finer material washed out. (FILL)
4													3.00-11.70m: wash boring
5													
6													
7													
8													
9													
10													

- SMALL DISTURBED SAMPLE
- LARGE DISTURBED SAMPLE
- SPT LINER SAMPLE
- U76 UNDISTURBED SAMPLE
- U100 UNDISTURBED SAMPLE
- MAZIER SAMPLE (70mm)
- PISTON SAMPLE
- WATER SAMPLE
- PIEZOMETER TIP
- STANDPIPE
- STANDARD PENETRATION TEST
- PERMEABILITY TEST
- IN-SITU VANE SHEAR TEST

LOGGED BENNY WONG
DATE 05/08/96
APPROVED C. LUN
DATE 06/08/96

REMARKS
Hole termination depth at 24.98m.
Inspection pit 0.00m to 2.00m.



BACHY SOLETANCHE GROUP
SOIL & FOUNDATIONS SPECIALISTS

DRILLHOLE RECORD

HOLE NO. P64

SHEET 2 of 3

CONTRACT

PROJECT LINCOLN HOUSE DEVELOPMENT, QUARRY BAY

METHOD ROTARY

CO-ORDINATES

W.O. W-518

MACHINE & No. D-17

E 839928.08

DATE from 17/7/96 to 18/7/96

N 816490.56

FLUSHING MEDIUM WATER

ORIENTATION Vertical

GROUND-LEVEL 4.54 mPD

Drilling Progress	Casing size	Water level (m) Shift start/end	Total core Recovery %	Solid core Recovery %	R.Q.D.	Fracture Index	Tests	Samples	Reduced Level	Depth (m)	Legend	Grade	Description
11													
12			40					T2-101	-7.16	11.70	+	IV/III	Moderately strong to moderately weak, brownish grey, spotted yellow, moderately to highly decomposed medium grained GRANITE with closely spaced, narrow to very narrow, rough undulating, limonite and stained joint, dipping 15° to 35°.
13									-7.66	12.20	+		12.20-16.00m: wash boring
14													
15													
16	HX 16.00m NX								-11.46	16.00	+	III	Moderately strong, pinkish grey, spotted black and white, moderately decomposed medium grained GRANITE with closely spaced, narrow to very narrow, rough undulating, limonite and manganese stained joints, dipping 5° to 25°.
17			100	98	72	10.5		TNW	-12.99	17.53	+		17.53-17.87m: wash boring
18	NX 17.87m								-13.33	17.87	+	III/II	Strong to moderately strong, pinkish grey, spotted black and white, slightly to moderately decomposed medium grained GRANITE with closely to medium spaced, very narrow, rough undulating, limonite and manganese stained joints, dipping 5° to 15°.
19			100	100	63	8.3		TNW	-14.66	19.20	+	II	Strong, pinkish grey, spotted black and white, slightly decomposed
20			100	100	98			TNW			+		

- SMALL DISTURBED SAMPLE
- LARGE DISTURBED SAMPLE
- SPT LINER SAMPLE
- U76 UNDISTURBED SAMPLE
- U100 UNDISTURBED SAMPLE
- MAZIER SAMPLE (70mm)
- PISTON SAMPLE
- WATER SAMPLE
- PIEZOMETER TIP
- STANDPIPE
- STANDARD PENETRATION TEST
- PERMEABILITY TEST
- IN-SITU VANE SHEAR TEST

LOGGED BENNY WONG

DATE 05/08/96

APPROVED C. LUN

DATE 06/08/96

REMARKS



BACHY SOLETANCHE GROUP
SOIL & FOUNDATIONS SPECIALISTS

DRILLHOLE RECORD

HOLE NO. P64

CONTRACT

SHEET 3 of 3

PROJECT LINCOLN HOUSE DEVELOPMENT, QUARRY BAY

METHOD ROTARY

CO-ORDINATES

W.O. W-518

MACHINE & No. D-17

E 839928.08

N 816490.56

DATE from 17/7/96 to 18/7/96

FLUSHING MEDIUM WATER

ORIENTATION Vertical

GROUND-LEVEL 4.54 mPD

Drilling Progress	Casing size	Water level (m) Shift start/end	Total core Recovery %	Solid core Recovery %	R.Q.D.	Fracture Index	Tests	Samples	Reduced Level	Depth (m)	Legend	Grade	Description
21			100	97	97			TNW		20.09	+		medium grained GRANITE with closely to medium spaced, extremely narrow, rough undulating, clean joints, dipping 5° to 10°. 22.00-23.53m: moderately strong to strong, moderately to slightly decomposed zone.
			100	100	100			TNW		20.70	+		
								TNW		21.50	+		
22			100	100	95	4.0		TNW	-17.46	22.00	+	III/II	
23								TNW		23.03	+		
			100	100	85			TNW	-18.99	23.53	+	II	
24								TNW		24.13	+		End of hole at 24.98m.
			100	100	100			TNW		24.98	+		
25													
26													
27													
28													
29													
30													

- SMALL DISTURBED SAMPLE
- LARGE DISTURBED SAMPLE
- SPT LINER SAMPLE
- U76 UNDISTURBED SAMPLE
- U100 UNDISTURBED SAMPLE
- MAZIER SAMPLE (70mm)
- PISTON SAMPLE
- WATER SAMPLE
- PIEZOMETER TIP
- STANDPIPE
- STANDARD PENETRATION TEST
- PERMEABILITY TEST
- IN-SITU VANE SHEAR TEST



LOGGED BENNY WONG

DATE 05/08/96

APPROVED C. LUN

DATE 06/08/96

REMARKS

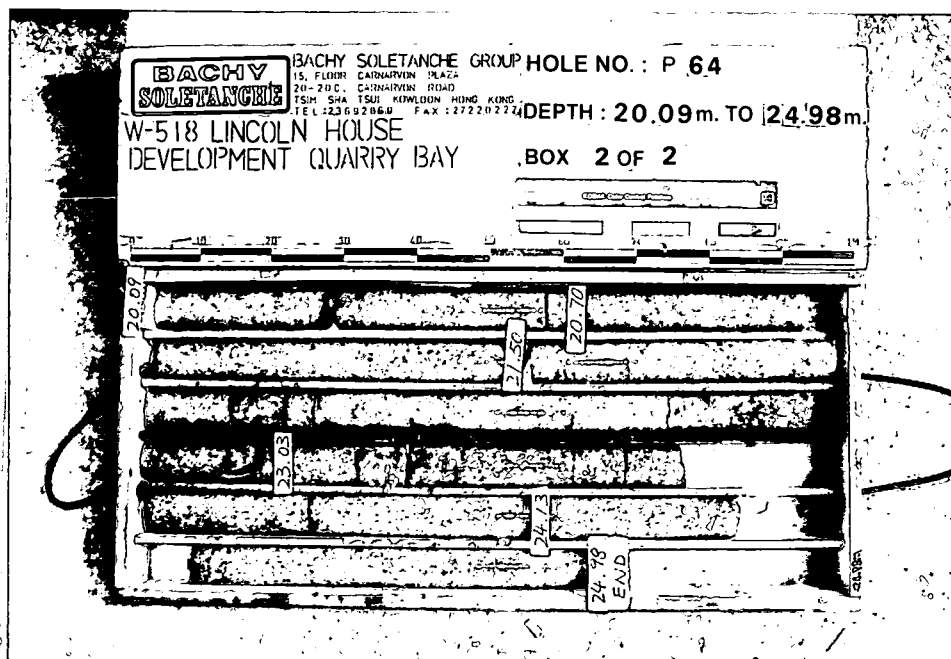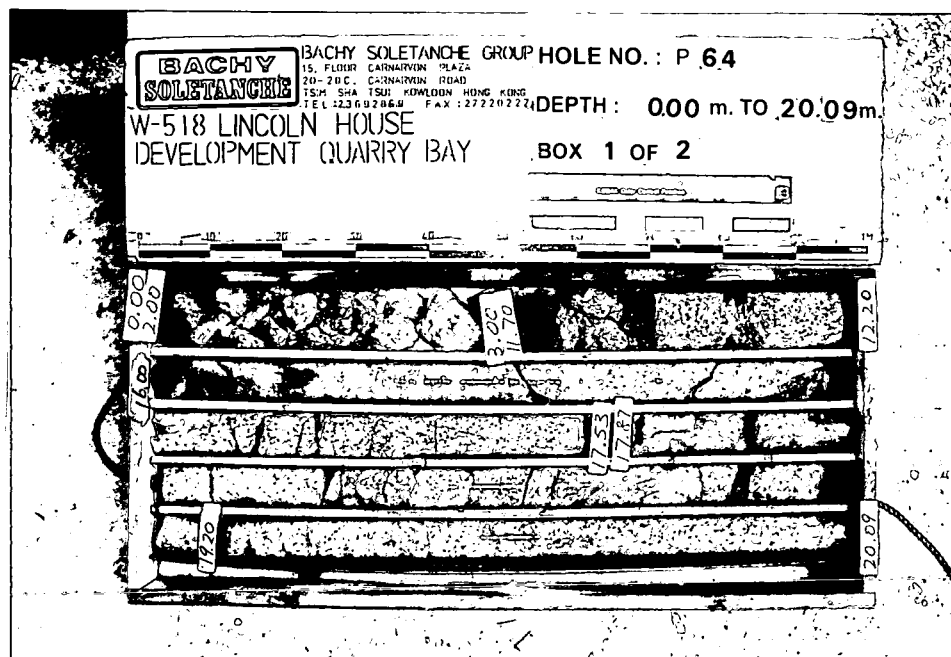



BACHY SOLETANCHE GROUP
SOIL & FOUNDATIONS SPECIALISTS

DRILLHOLE RECORD

HOLE NO. B6a

CONTRACT

SHEET 1 of 3

PROJECT LINCOLN HOUSE DEVELOPMENT, QUARRY BAY

METHOD ROTARY

CO-ORDINATES

W.O. W-518

MACHINE & No. D-12

E 839910.71

DATE from 18/7/96 to 20/7/96

N 816492.51

FLUSHING MEDIUM WATER

ORIENTATION Vertical

GROUND-LEVEL 4.60 mPD

Drilling Progress	Casing size	Water level (m) Shift start/end	Total core Recovery %	Solid core Recovery %	R.Q.D.	Fracture Index	Tests	Samples	Reduced Level	Depth (m)	Legend	Grade	Description
1	PX							INSPECTION PIT					0.00-2.50m: wash boring
2									2.10	2.50			
3	PX 3.00m HX		88					PX	1.70	2.90			Rounded to subrounded, COBBLES and fine to coarse GRAVEL. No recovery assumed, finer material washed out. (FILL) 2.90-14.90m: wash boring.
4													
5													
6													
7													
8													
9													
10													

- SMALL DISTURBED SAMPLE
- LARGE DISTURBED SAMPLE
- SPT LINER SAMPLE
- U76 UNDISTURBED SAMPLE
- U100 UNDISTURBED SAMPLE
- MAZIER SAMPLE (70mm)
- PISTON SAMPLE
- WATER SAMPLE
- PIEZOMETER TIP
- STANDPIPE
- STANDARD PENETRATION TEST
- PERMEABILITY TEST
- IN-SITU VANE SHEAR TEST

LOGGED BENNY WONG

DATE 05/08/96

APPROVED C. LUN

DATE 06/08/96

REMARKS

Hole termination depth at 28.50m.
Inspection pit at 0.00m to 2.00m.



BACHY SOLETANCHE GROUP
SOIL & FOUNDATIONS SPECIALISTS

DRILLHOLE RECORD

HOLE NO. B6a

CONTRACT

SHEET 2 of 3

PROJECT LINCOLN HOUSE DEVELOPMENT, QUARRY BAY

METHOD ROTARY

CO-ORDINATES

W.O. W-518

MACHINE & No. D-12

E 839910.71
N 816492.51

DATE from 18/7/96 to 20/7/96

FLUSHING MEDIUM WATER

ORIENTATION Vertical

GROUND-LEVEL 4.60 mPD

Drilling Progress	Casing size	Water level (m) Shift start/end	Total core Recovery %	Solid core Recovery %	R.Q.D.	Fracture Index	Tests	Samples	Reduced Level	Depth (m)	Legend	Grade	Description
11													
12													
13													
14													
15	HX 14.90m NX		81	75	52				-10.30	14.90	+	IV/III	Moderately strong to moderately weak, brownish grey, spotted black and white, moderately to highly decomposed, medium grained GRANITE with closely spaced, narrow to very narrow, rough undulating, limonite and manganese stained joints, dipping 15° to 35°.
16									-11.30	15.90	+		15.90-20.55m: wash boring
17													
18													
19													
20													

- SMALL DISTURBED SAMPLE
- ▬ LARGE DISTURBED SAMPLE
- ▨ SPT LIVER SAMPLE
- ▨ U76 UNDISTURBED SAMPLE
- ▨ U100 UNDISTURBED SAMPLE
- ▨ MAZIER SAMPLE (70mm)
- ▨ PISTON SAMPLE
- ▲ WATER SAMPLE
- ▲ PIEZOMETER TIP
- ▲ STANDPIPE
- ↓ STANDARD PENETRATION TEST
- ⊥ PERMEABILITY TEST
- ∇ IN-SITU VANE SHEAR TEST

LOGGED BENNY WONG

DATE 05/08/96

APPROVED C. LUN

DATE 06/08/96

REMARKS



BACHY SOLETANCHE GROUP
SOIL & FOUNDATIONS SPECIALISTS

DRILLHOLE RECORD

HOLE NO. B6a

CONTRACT

SHEET 3 of 3

PROJECT LINCOLN HOUSE DEVELOPMENT, QUARRY BAY

METHOD ROTARY

CO-ORDINATES

W.O. W-518

MACHINE & No. D-12

E 839910.71
N 816492.51

DATE from 18/7/96 to 20/7/96

FLUSHING MEDIUM WATER

ORIENTATION Vertical

GROUND-LEVEL 4.60 mPD

Drilling Progress	Casing size	Water level (m) Shift start/end	Total core Recovery %	Solid core Recovery %	R.Q.D.	Fracture Index	Tests	Samples	Reduced Level	Depth (m)	Legend	Grade	Description
21	NX 20.55m		90	90	90	5.8		T2 -101	-15.95	20.55	+	II/III	Moderately strong to strong, pinkish grey, spotted black and white, moderately to slightly decomposed medium grained GRANITE with closely to extremely closely spaced, narrow to very narrow, rough undulating, limonite and manganese stained joints, dipping 15° to 35°. 21.58-21.76m: no recovery assumed highly decomposed zone. 21.76-22.72m: moderately strong to weak, moderately to highly decomposed zone. Moderately strong to strong, pinkish grey, spotted black and white, moderately to slightly decomposed medium grained GRANITE with closely spaced, very narrow to extremely narrow, rough undulating, limonite and manganese stained joints, dipping 5° to 10°.
			98	98	72			T2 -101	-16.98	21.15	+		
			0	0	0	NR		T2 -101	-17.16	21.58	+	IV	
22			86	42	17	17.5		T2 -101	-17.16	21.76	+	III/IV	
						NI			-18.12	22.16	+		
									-18.12	22.72	+	III/II	
23			100	97	70			T2 -101			+		
24			100	100	70			T2 -101		23.89	+		
25			100	100	100	4.8		T2 -101		24.82	+		
26			100	100	93			T2 -101		26.30	+		
27			100	100	100			T2 -101		27.38	+		
28									-23.90	28.50	+		End of hole at 28.50m.
29													
30													

- SMALL DISTURBED SAMPLE
- LARGE DISTURBED SAMPLE
- ▨ SPT LINER SAMPLE
- ▨ U76 UNDISTURBED SAMPLE
- ▨ U100 UNDISTURBED SAMPLE
- ▨ MAZIER SAMPLE (70mm)
- ▨ PISTON SAMPLE
- Δ WATER SAMPLE
- ▲ PIEZOMETER TIP
- STANDPIPE
- ↓ STANDARD PENETRATION TEST
- ⊥ PERMEABILITY TEST
- ∇ IN-SITU VANE SHEAR TEST



LOGGED BENNY WONG

DATE 05/08/96

APPROVED C. LUN

DATE 06/08/96

REMARKS

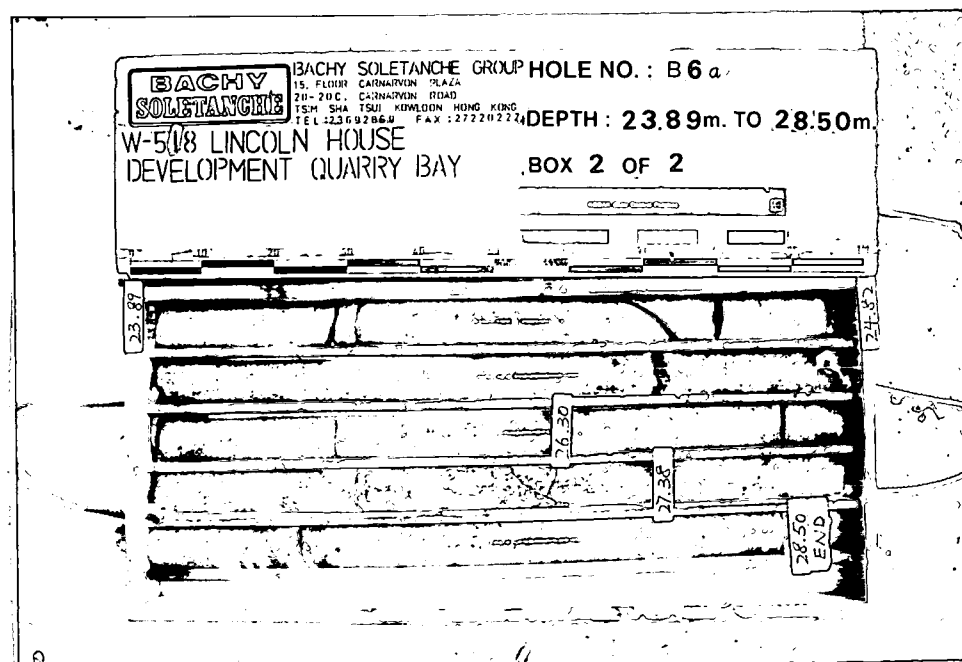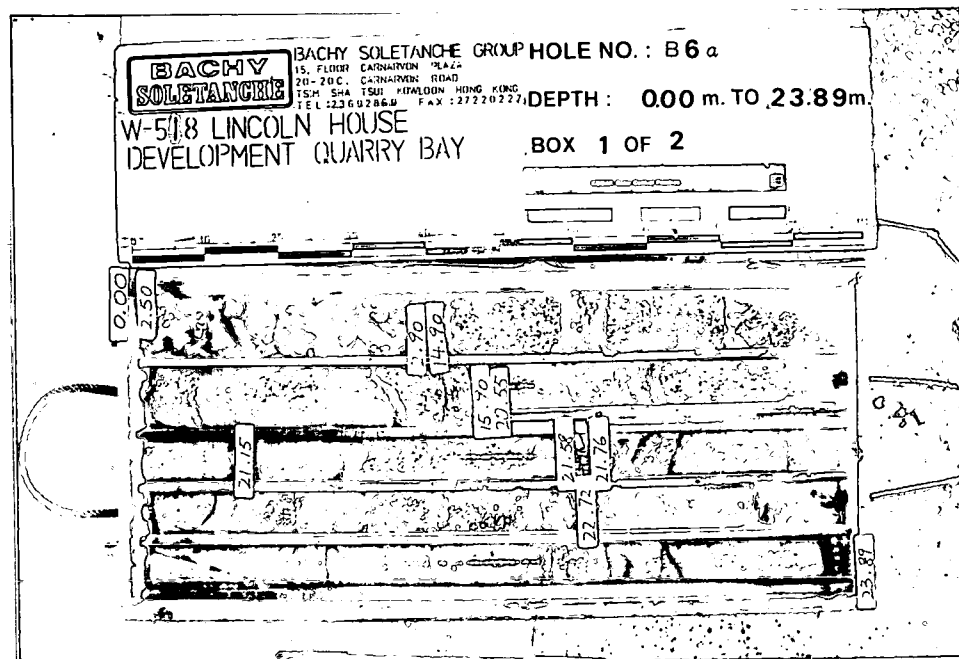



BACHY SOLETANCHE GROUP
SOIL & FOUNDATIONS SPECIALISTS

DRILLHOLE RECORD

HOLE NO. B6b

SHEET 1 of 4

CONTRACT

PROJECT LINCOLN HOUSE DEVELOPMENT, QUARRY BAY

METHOD ROTARY

CO-ORDINATES

W.O. W-518

MACHINE & No.

E 839902.31

DATE from 22/7/96 to 23/7/96

N 816492.74

FLUSHING MEDIUM WATER

ORIENTATION Vertical

GUIDE WALL LEVEL 4.61 mPD

Drilling Progress	Casing size	Water level (m) Shift start/end	Total core Recovery %	Solid core Recovery %	R.Q.D.	Fracture Index	Tests	Samples	Reduced Level	Depth (m)	Legend	Grade	Description
1	PX							INSPECTION PIT		0.00			Wash boring.
2										2.00			
3													
4													
5	PX 5.00m HX												
6													
7													
8													
9													
10													

- SMALL DISTURBED SAMPLE
- LARGE DISTURBED SAMPLE
- SPT LINER SAMPLE
- U76 UNDISTURBED SAMPLE
- U100 UNDISTURBED SAMPLE
- MAZIER SAMPLE (70mm)
- PISTON SAMPLE
- WATER SAMPLE
- PIEZOMETER TIP
- STANDPIPE
- STANDARD PENETRATION TEST
- PERMEABILITY TEST
- IN-SITU VANE SHEAR TEST

LOGGED BENNY WONG

DATE 24/07/96

APPROVED C.LUN

DATE 25/07/96

REMARKS

Hole termination depth at 30.41m.
Inspection pit from 0.00m to 2.00m.



BACHY SOLETANCHE GROUP
SOIL & FOUNDATIONS SPECIALISTS

DRILLHOLE RECORD

HOLE NO. B6b

SHEET 2 of 4

CONTRACT

PROJECT LINCOLN HOUSE DEVELOPMENT, QUARRY BAY

METHOD ROTARY

CO-ORDINATES

W.O. W-518

MACHINE & No.

E 839902.31
N 816492.74

DATE from 22/7/96 to 23/7/96

FLUSHING MEDIUM WATER

ORIENTATION Vertical

GUIDE WALL LEVEL 4.61 mPD

Drilling Progress	Casing size	Water level (m) Shift start/end	Total core Recovery %	Solid core Recovery %	R.Q.D.	Fracture Index	Tests	Samples	Reduced Level	Depth (m)	Legend	Grade	Description
11													AS SHEET 1 OF 4.
12													
13													
14													
15													
16													
17													
18													
19													
20													

- SMALL DISTURBED SAMPLE
- LARGE DISTURBED SAMPLE
- SPT LINER SAMPLE
- U76 UNDISTURBED SAMPLE
- U100 UNDISTURBED SAMPLE
- MAZIER SAMPLE (70mm)
- PISTON SAMPLE
- WATER SAMPLE
- PIEZOMETER TIP
- STANDPIPE
- STANDARD PENETRATION TEST
- PERMEABILITY TEST
- IN-SITU VANE SHEAR TEST

LOGGED BENNY WONG

DATE 24/07/96

APPROVED C.LUN

DATE 25/07/96

REMARKS



BACHY SOLETANCHE GROUP
SOIL & FOUNDATIONS SPECIALISTS

DRILLHOLE RECORD

HOLE NO. B6b

CONTRACT

SHEET 3 of 4

PROJECT LINCOLN HOUSE DEVELOPMENT, QUARRY BAY

METHOD ROTARY

CO-ORDINATES

W.O. W-518

MACHINE & No.

E 839902.31
N 816492.74

DATE from 22/7/96 to 23/7/96

FLUSHING MEDIUM WATER

ORIENTATION Vertical

GROUND-LEVEL 4.61 mPD

Drilling Progress	Casing size	Water level (m) Shift start/end	Total core Recovery %	Solid core Recovery %	R.Q.D.	Fracture Index	Tests	Samples	Reduced Level	Depth (m)	Legend	Grade	Description
21	HX 21.00m NX												AS SHEET 2 OF 4.
22													
23													
24	NX 24.32m								-19.71	24.32			
25			100	98	85			TNW				III	Moderately strong, brownish grey spotted yellow, moderately decomposed, medium grained GRANITE with closely spaced, narrow to very narrow, rough undulating, limonite and manganese stained joints, dipping 15°-35°.
26								TNW		25.80			
27			100	100	58	5.3		TNW		27.36			
28			100	100	91			TNW	-23.29	27.90		II	Strong, pinkish grey spotted black, slightly decomposed, medium grained GRANITE, with closely to medium spaced, rough undulating, extremely narrow, clean, joints, dipping 5°-10°.
29			100	100	100			TNW		28.88			
30			100	100	100	2.5		TNW		29.61			
										30.00			

- SMALL DISTURBED SAMPLE
- LARGE DISTURBED SAMPLE
- SPT LINER SAMPLE
- U76 UNDISTURBED SAMPLE
- U100 UNDISTURBED SAMPLE
- MAZIER SAMPLE (70mm)
- PISTON SAMPLE
- Δ WATER SAMPLE
- ▲ PIEZOMETER TIP
- STANDPIPE
- STANDARD PENETRATION TEST
- PERMEABILITY TEST
- ∇ IN-SITU VANE SHEAR TEST

LOGGED BENNY WONG

DATE 24/07/96

APPROVED C.LUN

DATE 25/07/96

REMARKS



BACHY SOLETANCHE GROUP
SOIL & FOUNDATIONS SPECIALISTS

DRILLHOLE RECORD

CONTRACT

HOLE NO. B6b

SHEET 4 of 4

PROJECT LINCOLN HOUSE DEVELOPMENT, QUARRY BAY

METHOD ROTARY

CO-ORDINATES

W.O. W-518

MACHINE & No.

E 839902.31
N 816492.74

DATE from 22/7/96 to 23/7/96

FLUSHING MEDIUM WATER

ORIENTATION Vertical

GUIDE WALL LEVEL 4.61 mPD

Drilling Progress	Casing size	Water level (m) Shift start/end	Total core Recovery %	Solid core Recovery %	R.Q.D.	Fracture Index	Tests	Samples	Reduced Level	Depth (m)	Legend	Grade	Description
23/07			100	100	100	2.5		TNW	-25.80	30.41	++ ++ ++	II	AS SHEET 3 OF 4.
31													End of hole at 30.41m.
32													
33													
34													
35													
36													
37													
38													
39													
40													

- SMALL DISTURBED SAMPLE
- ▮ LARGE DISTURBED SAMPLE
- ▮ SPT LINER SAMPLE
- ▮ U76 UNDISTURBED SAMPLE
- ▮ U100 UNDISTURBED SAMPLE
- ▮ MAZIER SAMPLE (70mm)
- ▮ PISTON SAMPLE
- Δ WATER SAMPLE
- ▲ PIEZOMETER TIP
- STANDPIPE
- ↓ STANDARD PENETRATION TEST
- ⊥ PERMEABILITY TEST
- ∇ IN-SITU VANE SHEAR TEST



LOGGED BENNY WONG

DATE 24/07/96

APPROVED C.LUN

DATE 25/07/96

REMARKS

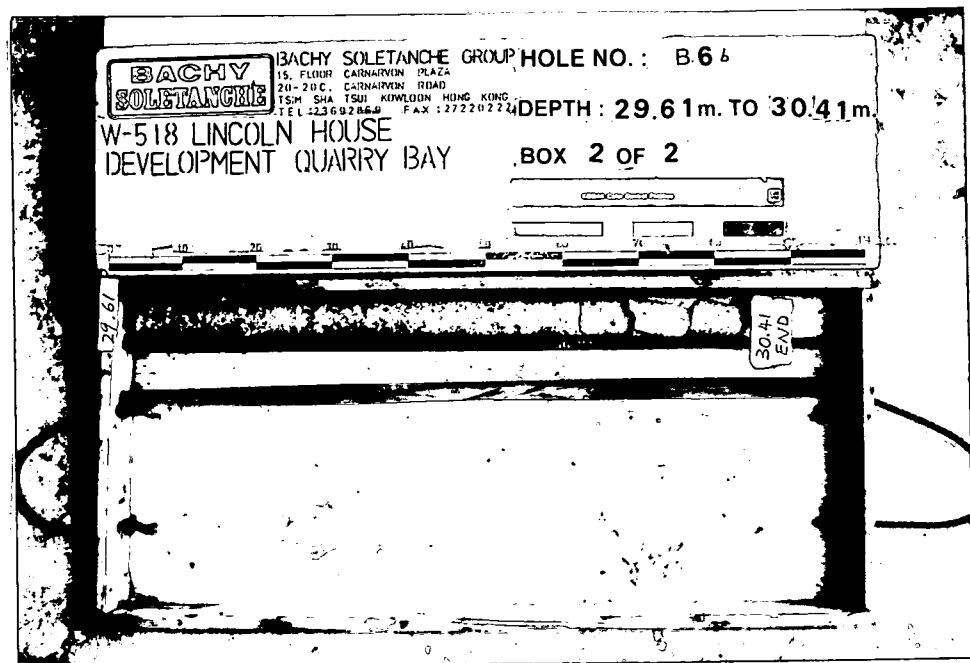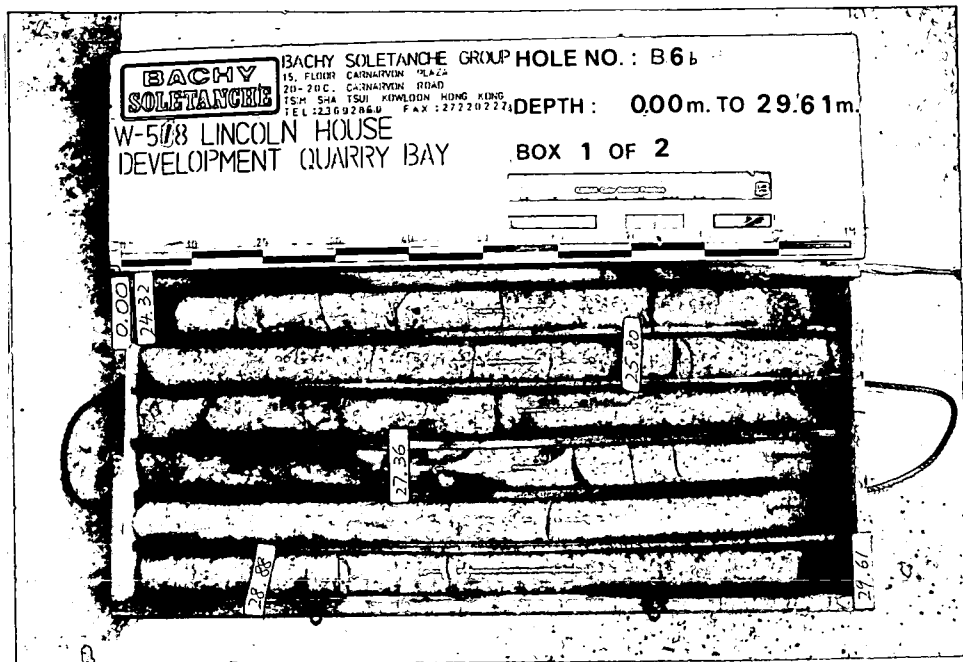



BACHY SOLETANCHE GROUP
SOIL & FOUNDATIONS SPECIALISTS

DRILLHOLE RECORD

HOLE NO. C6a

CONTRACT

SHEET 1 of 3

PROJECT LINCOLN HOUSE DEVELOPMENT, QUARRY BAY

METHOD ROTARY

CO-ORDINATES

W.O. W-518

MACHINE & No. D-12

E 839919.10
N 816492.29

DATE from 23/7/96 to 24/7/96

FLUSHING MEDIUM WATER

ORIENTATION Vertical

GUIDE WALL LEVEL 4.60 mPD

Drilling Progress	Casing size	Water level (m) Shift start/end	Total core Recovery %	Solid core Recovery %	R.Q.D.	Fracture Index	Tests	Samples	Reduced Level	Depth (m)	Legend	Grade	Description
1	PX								3.50	1.10			Wash boring.
2			42					HX	2.20	2.40			Rounded and sub-rounded COBBLES, fine to coarse GRAVEL and CONCRETE. No recovery, assumed finer material washed out. (FILL)
3	PX 3.00m HX												Wash boring.
4													
5													
6													
7													
8													
9													
10													

- ▲ SMALL DISTURBED SAMPLE
- LARGE DISTURBED SAMPLE
- ▨ SPT LINER SAMPLE
- ▩ U76 UNDISTURBED SAMPLE
- ▩ U100 UNDISTURBED SAMPLE
- ▩ MAZIER SAMPLE (70mm)
- ▩ PISTON SAMPLE
- △ WATER SAMPLE
- ▲ PIEZOMETER TIP
- STANDPIPE
- ⊥ STANDARD PENETRATION TEST
- ⊥ PERMEABILITY TEST
- ∇ IN-SITU VANE SHEAR TEST

LOGGED BENNY WONG

DATE 25/07/96

APPROVED C.LUN

DATE 26/07/96

REMARKS

Hole termination depth at 26.57m.



BACHY SOLETANCHE GROUP
SOIL & FOUNDATIONS SPECIALISTS

DRILLHOLE RECORD

HOLE NO. C6a

CONTRACT

SHEET 2 of 3

PROJECT LINCOLN HOUSE DEVELOPMENT, QUARRY BAY

METHOD ROTARY

CO-ORDINATES

W.O. W-518

MACHINE & No. D-12

E 839919.10

DATE from 23/7/96 to 24/7/96

N 816492.29

FLUSHING MEDIUM WATER

ORIENTATION Vertical

GUIDE WALL LEVEL 4.60 mPD

Drilling Progress	Casing size	Water level (m) Shift start/end	Total core Recovery %	Solid core Recovery %	R.Q.D.	Fracture Index	Tests	Samples	Reduced Level	Depth (m)	Legend	Grade	Description
11													AS SHEET 1 OF 3.
12													
13													
14													
15	HX 15.00m NX												
16													
17													
18													
19	NX 18.95m												
20													
24/07/96			97	46	26			T2-101	-14.35	18.95	+	III	Moderately strong, brownish grey spotted yellow, moderately decomposed, medium grained GRANITE with closely spaced, narrow to very narrow, rough
			100	100	100	14.1		T2-101	-15.20	19.34	+		
								T2-101		19.80	+	II/III	

- SMALL DISTURBED SAMPLE
- LARGE DISTURBED SAMPLE
- ▨ SPT LINER SAMPLE
- U76 UNDISTURBED SAMPLE
- U100 UNDISTURBED SAMPLE
- ▨ MAZIER SAMPLE (70mm)
- ▨ PISTON SAMPLE
- △ WATER SAMPLE
- ▲ PIEZOMETER TIP
- △ STANDPIPE
- ⊥ STANDARD PENETRATION TEST
- ⊥ PERMEABILITY TEST
- ∇ IN-SITU VANE SHEAR TEST

LOGGED BENNY WONG

DATE 25/07/96

APPROVED C.LUN

DATE 26/07/96

REMARKS



BACHY SOLETANCHE GROUP
SOIL & FOUNDATIONS SPECIALISTS

DRILLHOLE RECORD

HOLE NO. C6a

CONTRACT

SHEET 3 of 3

PROJECT LINCOLN HOUSE DEVELOPMENT, QUARRY BAY

METHOD ROTARY

CO-ORDINATES

W.O. W-518

MACHINE & No. D-12

E 839919.10
N 816492.29

DATE from 23/7/96 to 24/7/96

FLUSHING MEDIUM WATER

ORIENTATION Vertical

GUIDE WALL LEVEL 4.60 mPD

Drilling Progress	Casing size	Water level (m) Shift start/end	Total core Recovery %	Solid core Recovery %	R.Q.D.	Fracture Index	Tests	Samples	Reduced Level	Depth (m)	Legend	Grade	Description
21			99	99	99			T2 -101		20.88	++	II/III	undulating, limonite and manganese stained joints, dipping 15°-35°.
22			94	94	89			T2 -101		22.38	++		Moderately strong to strong, pinkish grey spotted black and white, moderately to slightly decomposed, medium grained GRANITE with closely to medium spaced, very narrow to extremely narrow, rough undulating, clean joints, dipping 5°-10°.
23			100	100	100	5.7		T2 -101		22.76	++		
24			99	99	99			T2 -101		23.89	++		
25			99	99	99			T2 -101		25.29	++		
26			98	78	77	8.6		T2 -101	-20.69	26.57	++	II/III	Strong to moderately strong, spotted black and white, slightly to moderately decomposed, medium grained GRANITE with closely to medium spaced, narrow to very narrow, rough undulating, limonite and manganese stained joints, dipping 5°-10° and 25°-35°.
27													End of hole at 26.37m.
28													
29													
30													

- SMALL DISTURBED SAMPLE
- LARGE DISTURBED SAMPLE
- SPT LINER SAMPLE
- U76 UNDISTURBED SAMPLE
- U100 UNDISTURBED SAMPLE
- MAZIER SAMPLE (70mm)
- PISTON SAMPLE
- WATER SAMPLE
- PIEZOMETER TIP
- STANDPIPE
- STANDARD PENETRATION TEST
- PERMEABILITY TEST
- IN-SITU VANE SHEAR TEST

LOGGED BENNY WONG
DATE 25/07/96
APPROVED C.LUN
DATE 26/07/96

REMARKS

